



Project Schedule(Level 3)




Project Schedule(Level 3)

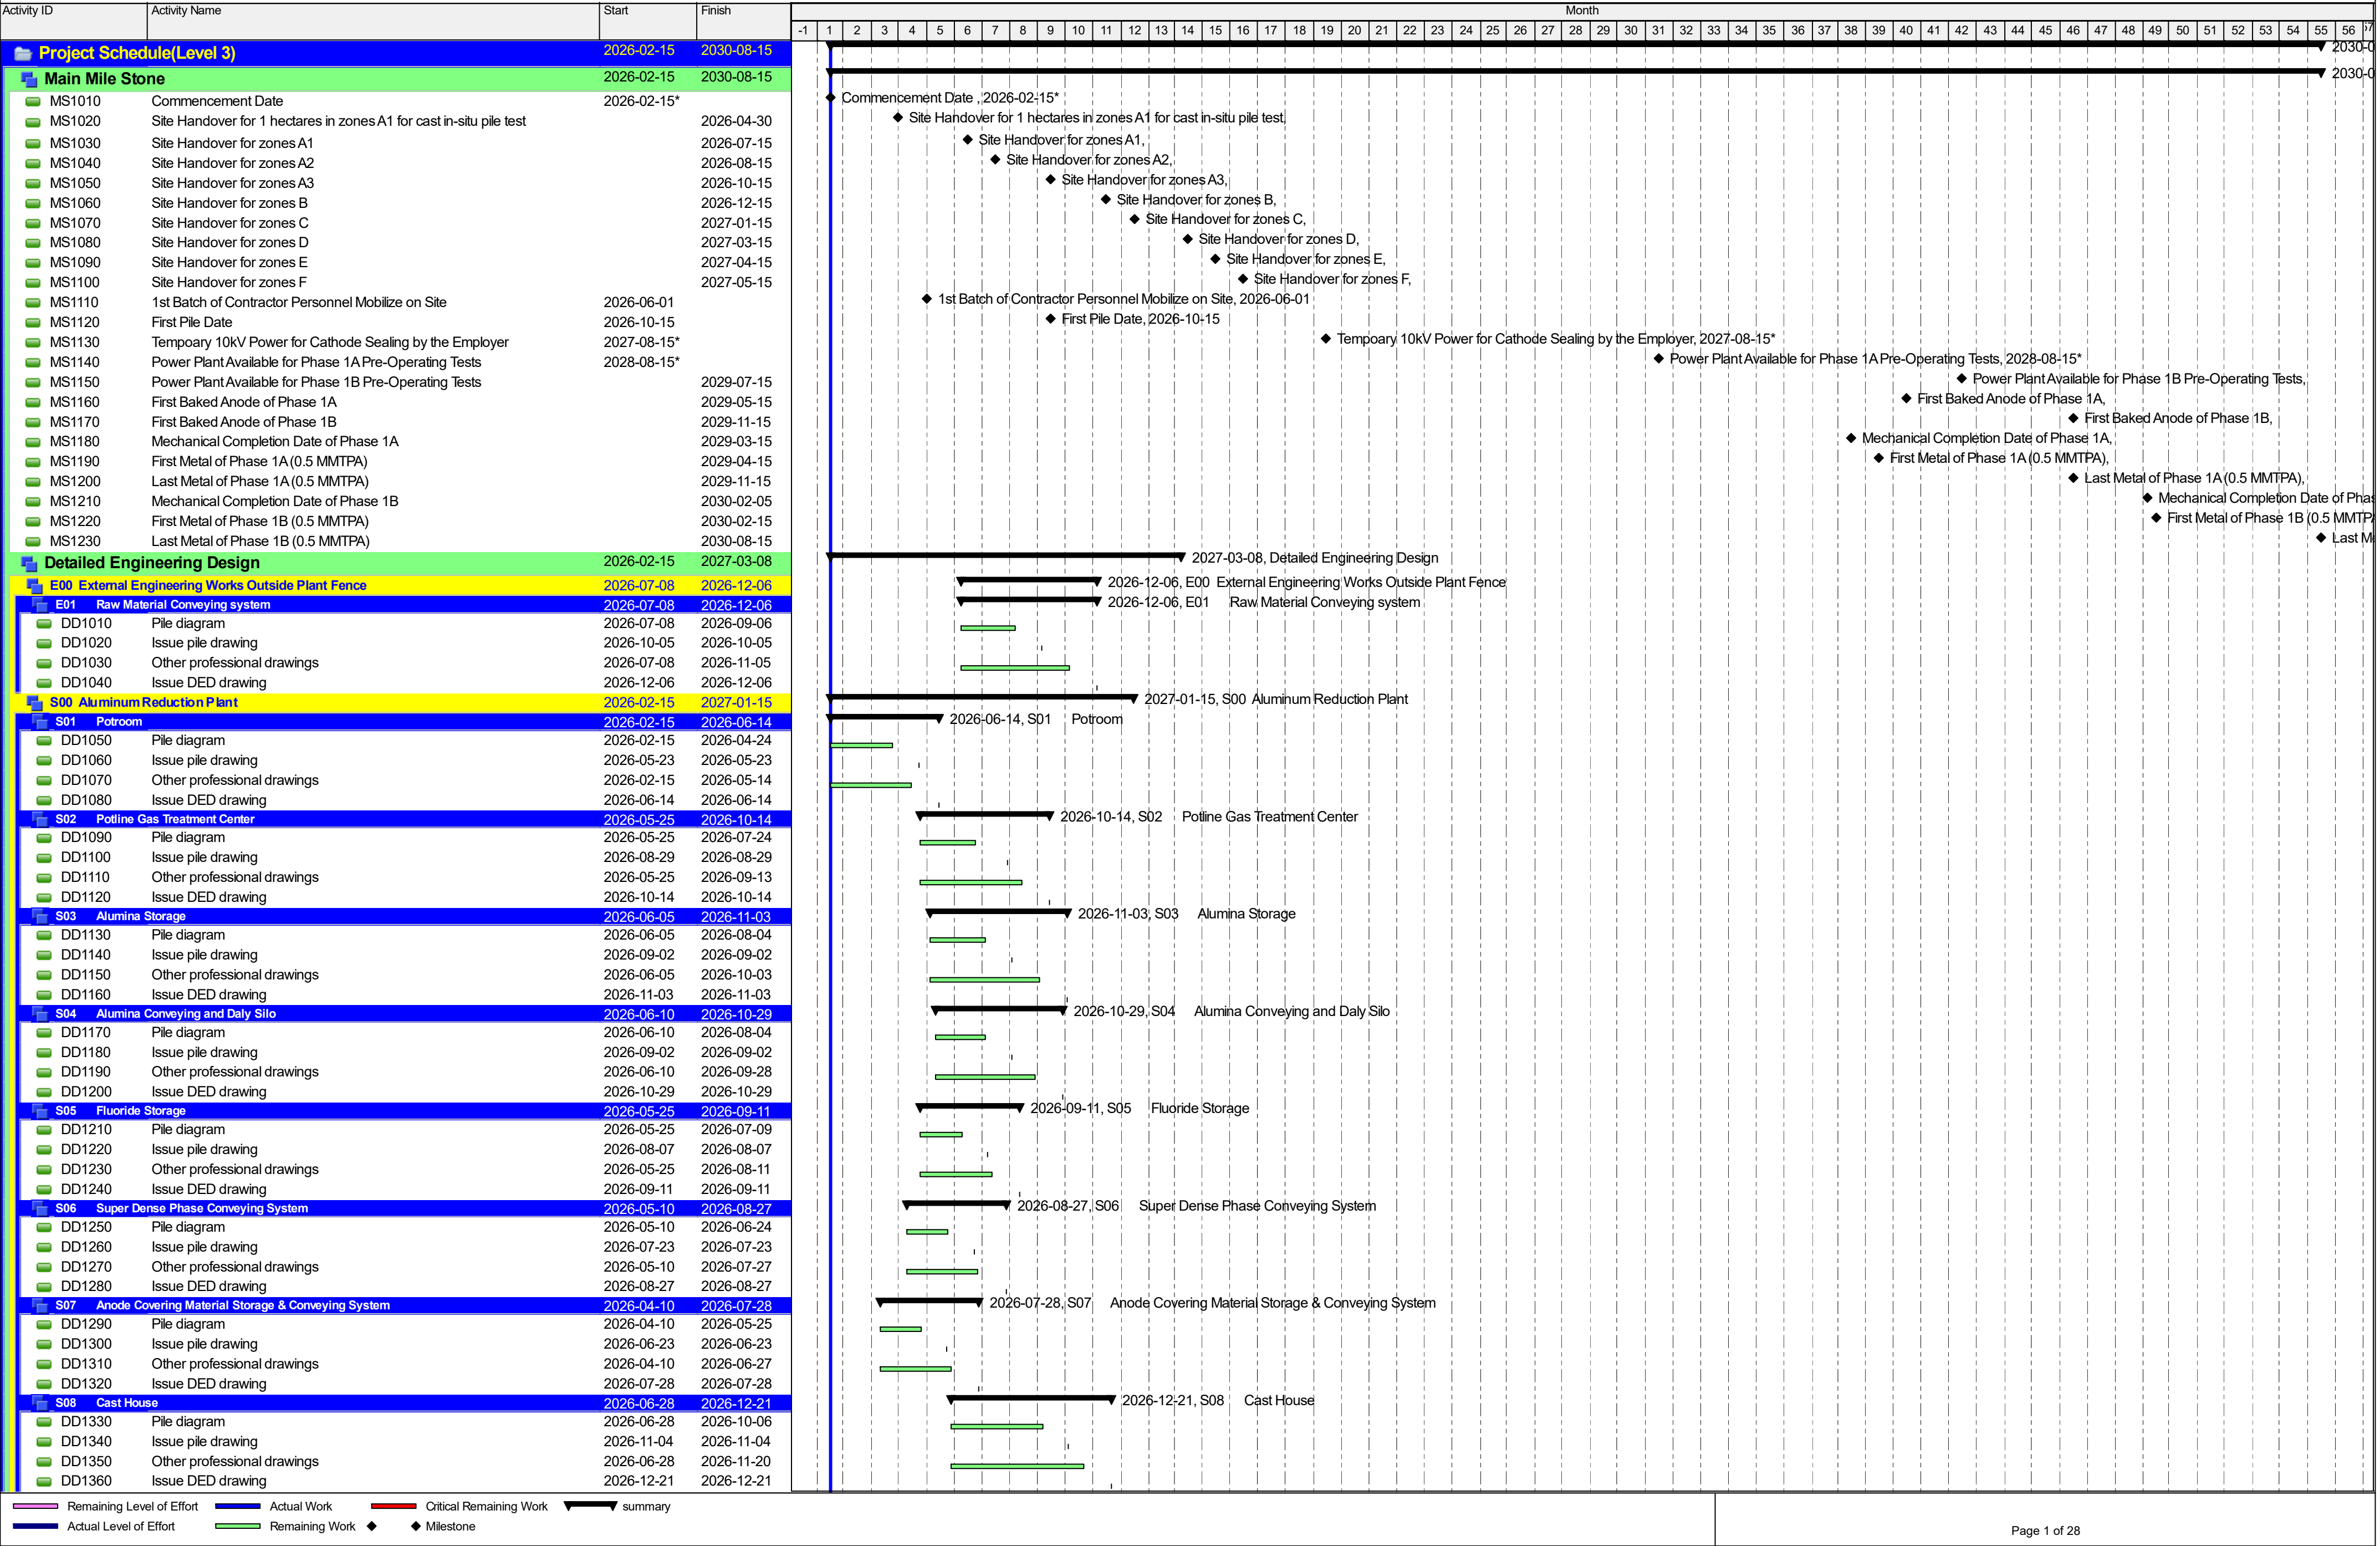

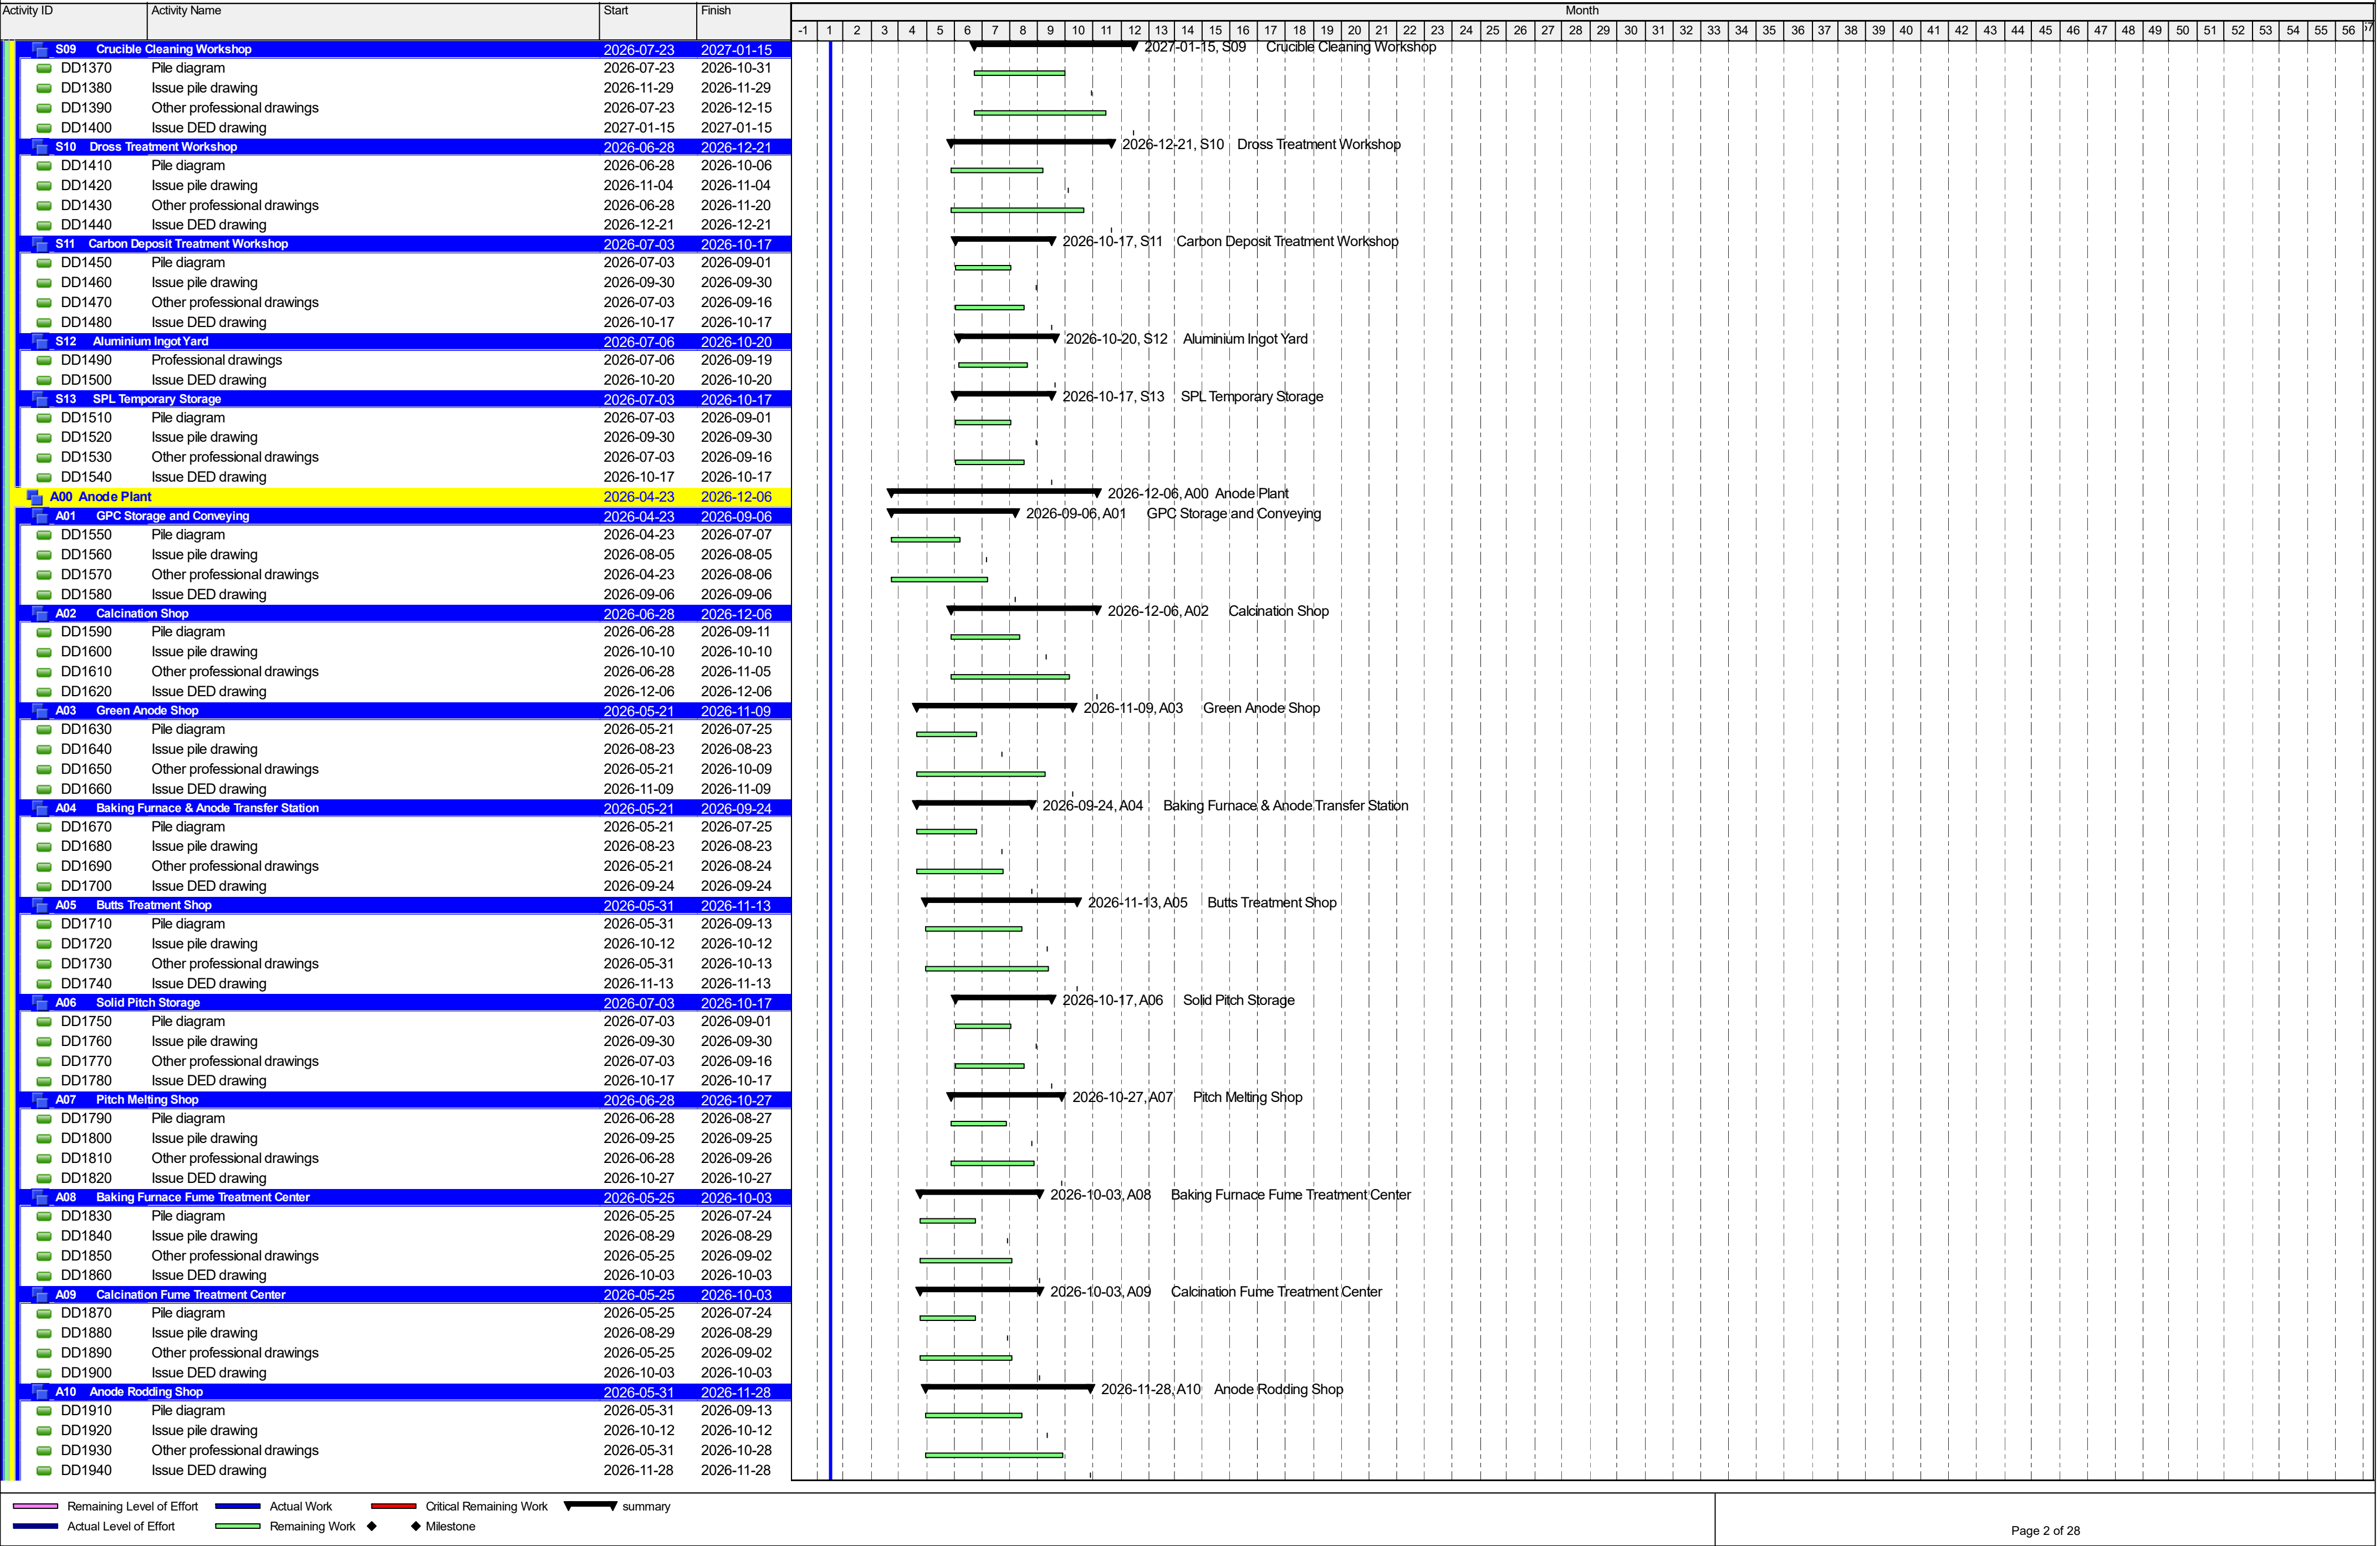

Project Schedule(Level 3)

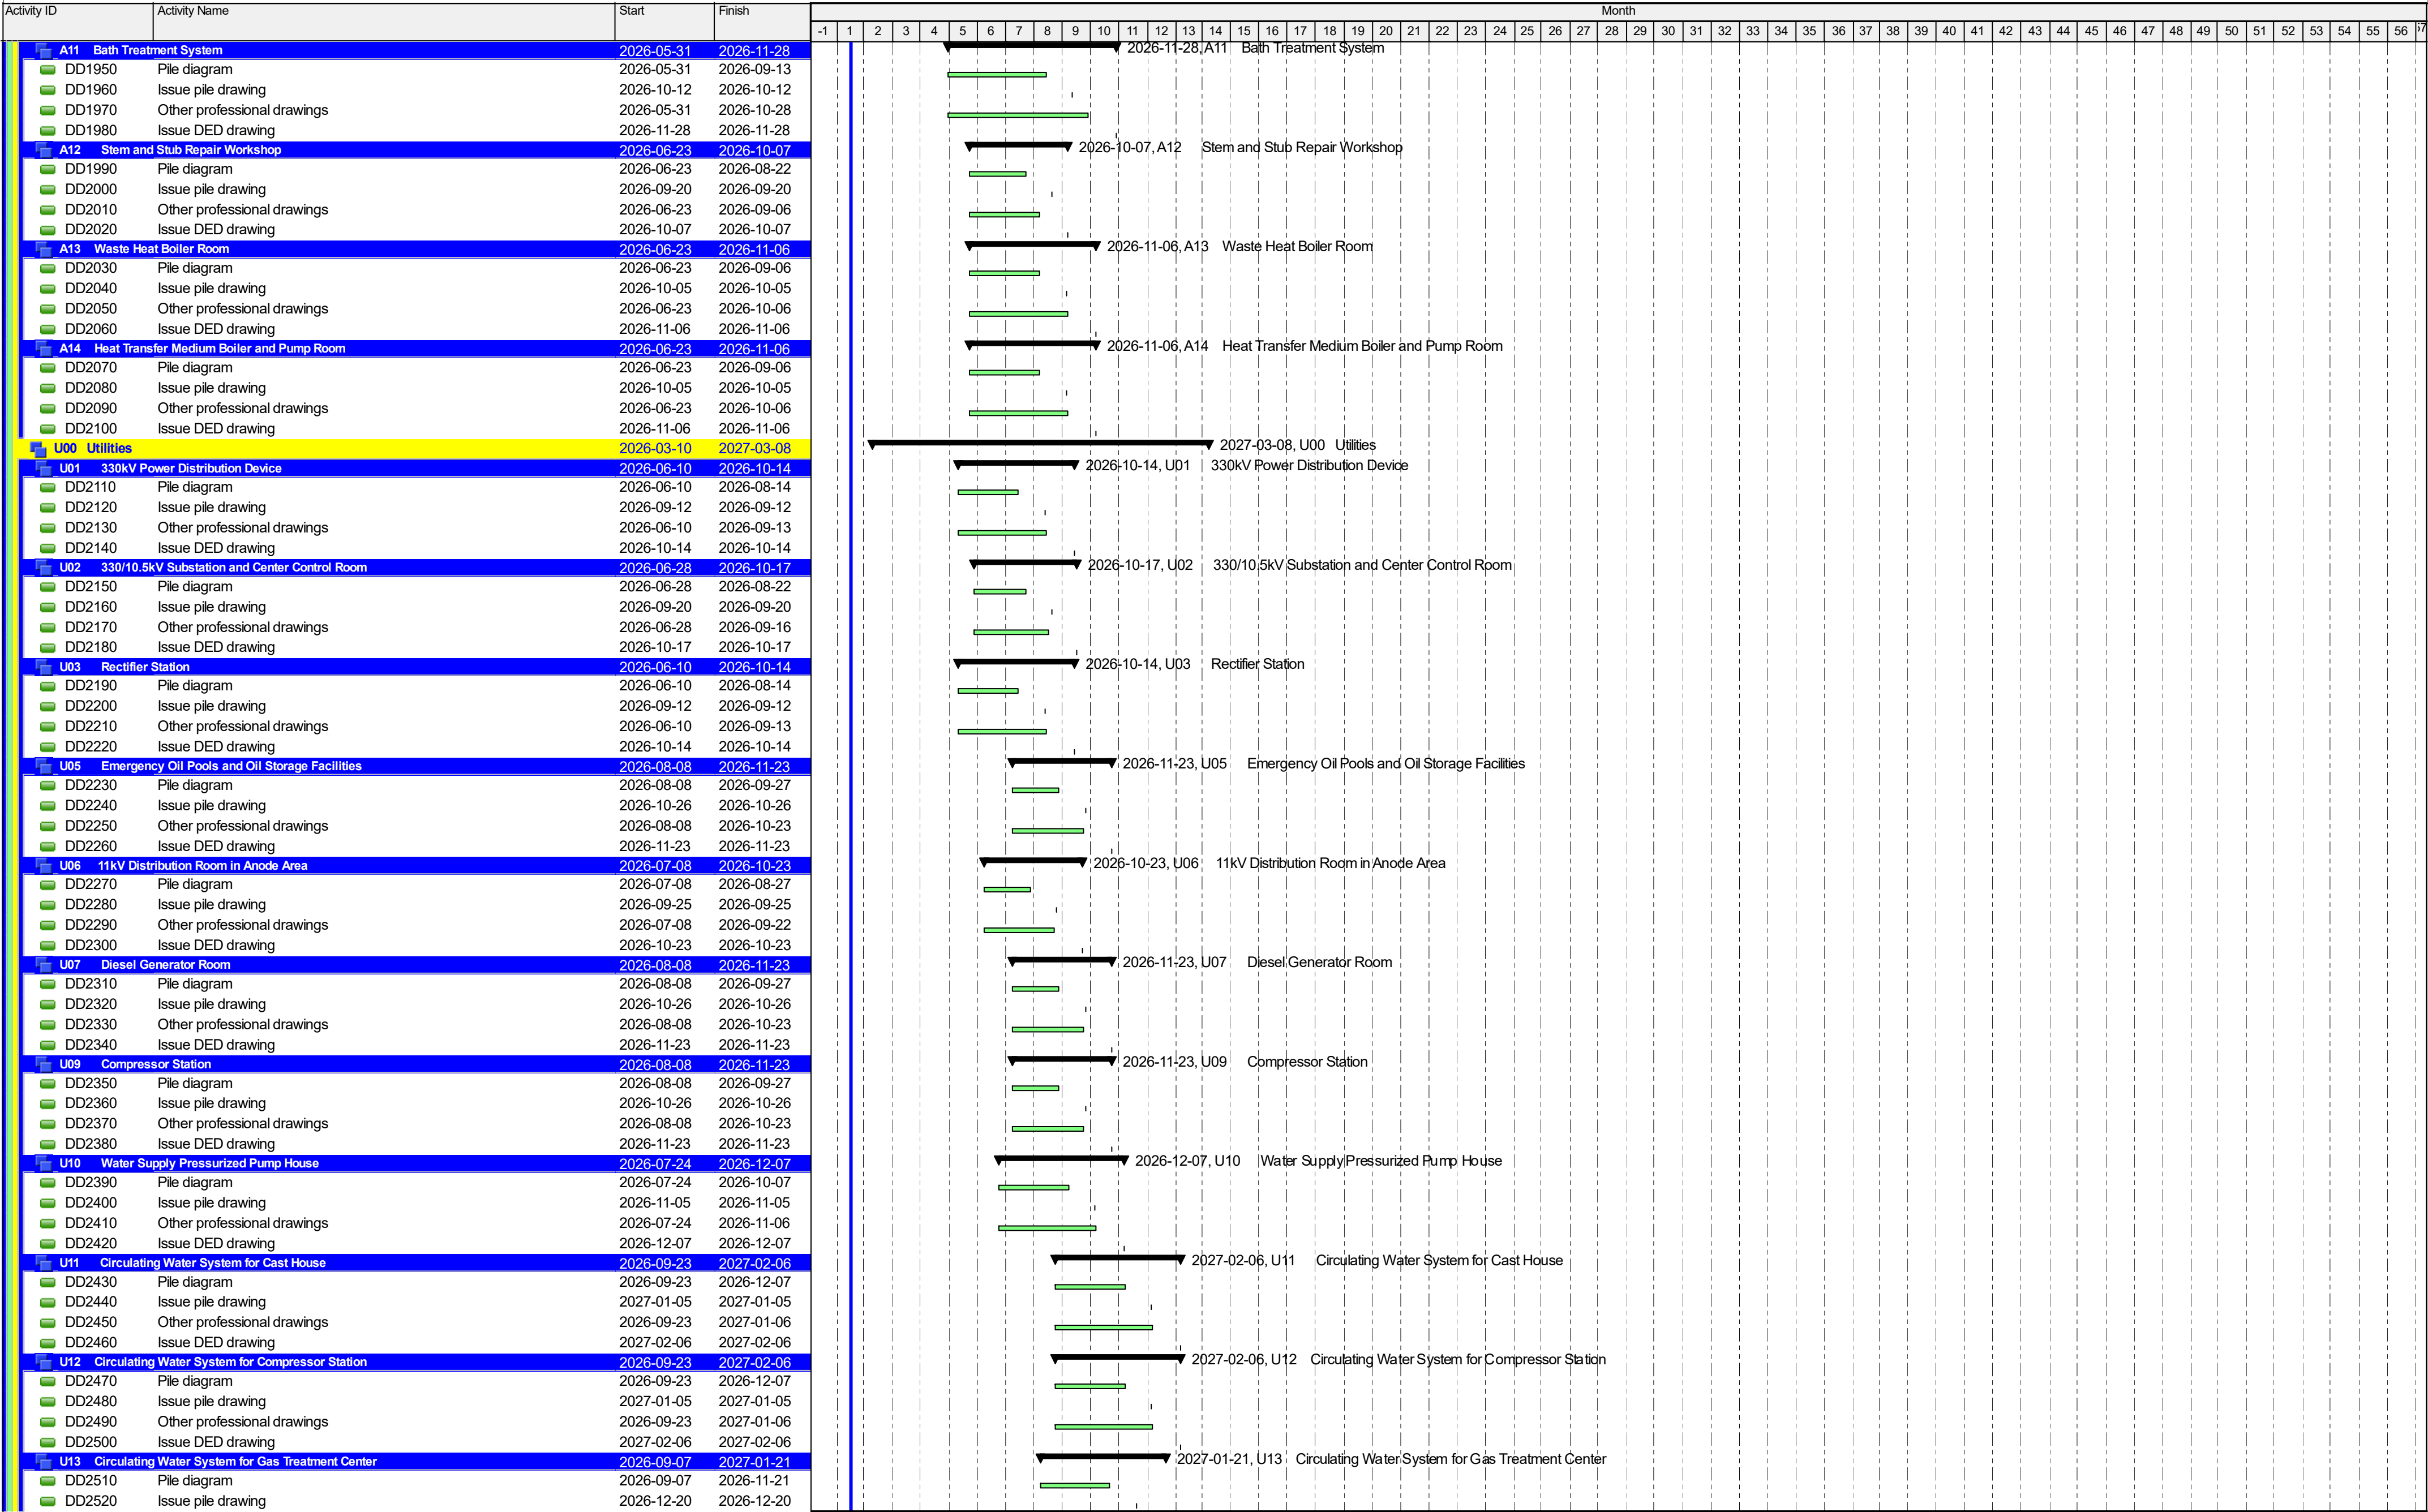

## Project Schedule(Level 3)

 Remaining Level of Effort
  Actual Work
  Critical Remaining Work
  summary

 Actual Level of Effort
  Remaining Work
  Milestone


Page 4 of 28



## Project Schedule(Level 3)

[illegible]

## Project Schedule(Level 3)

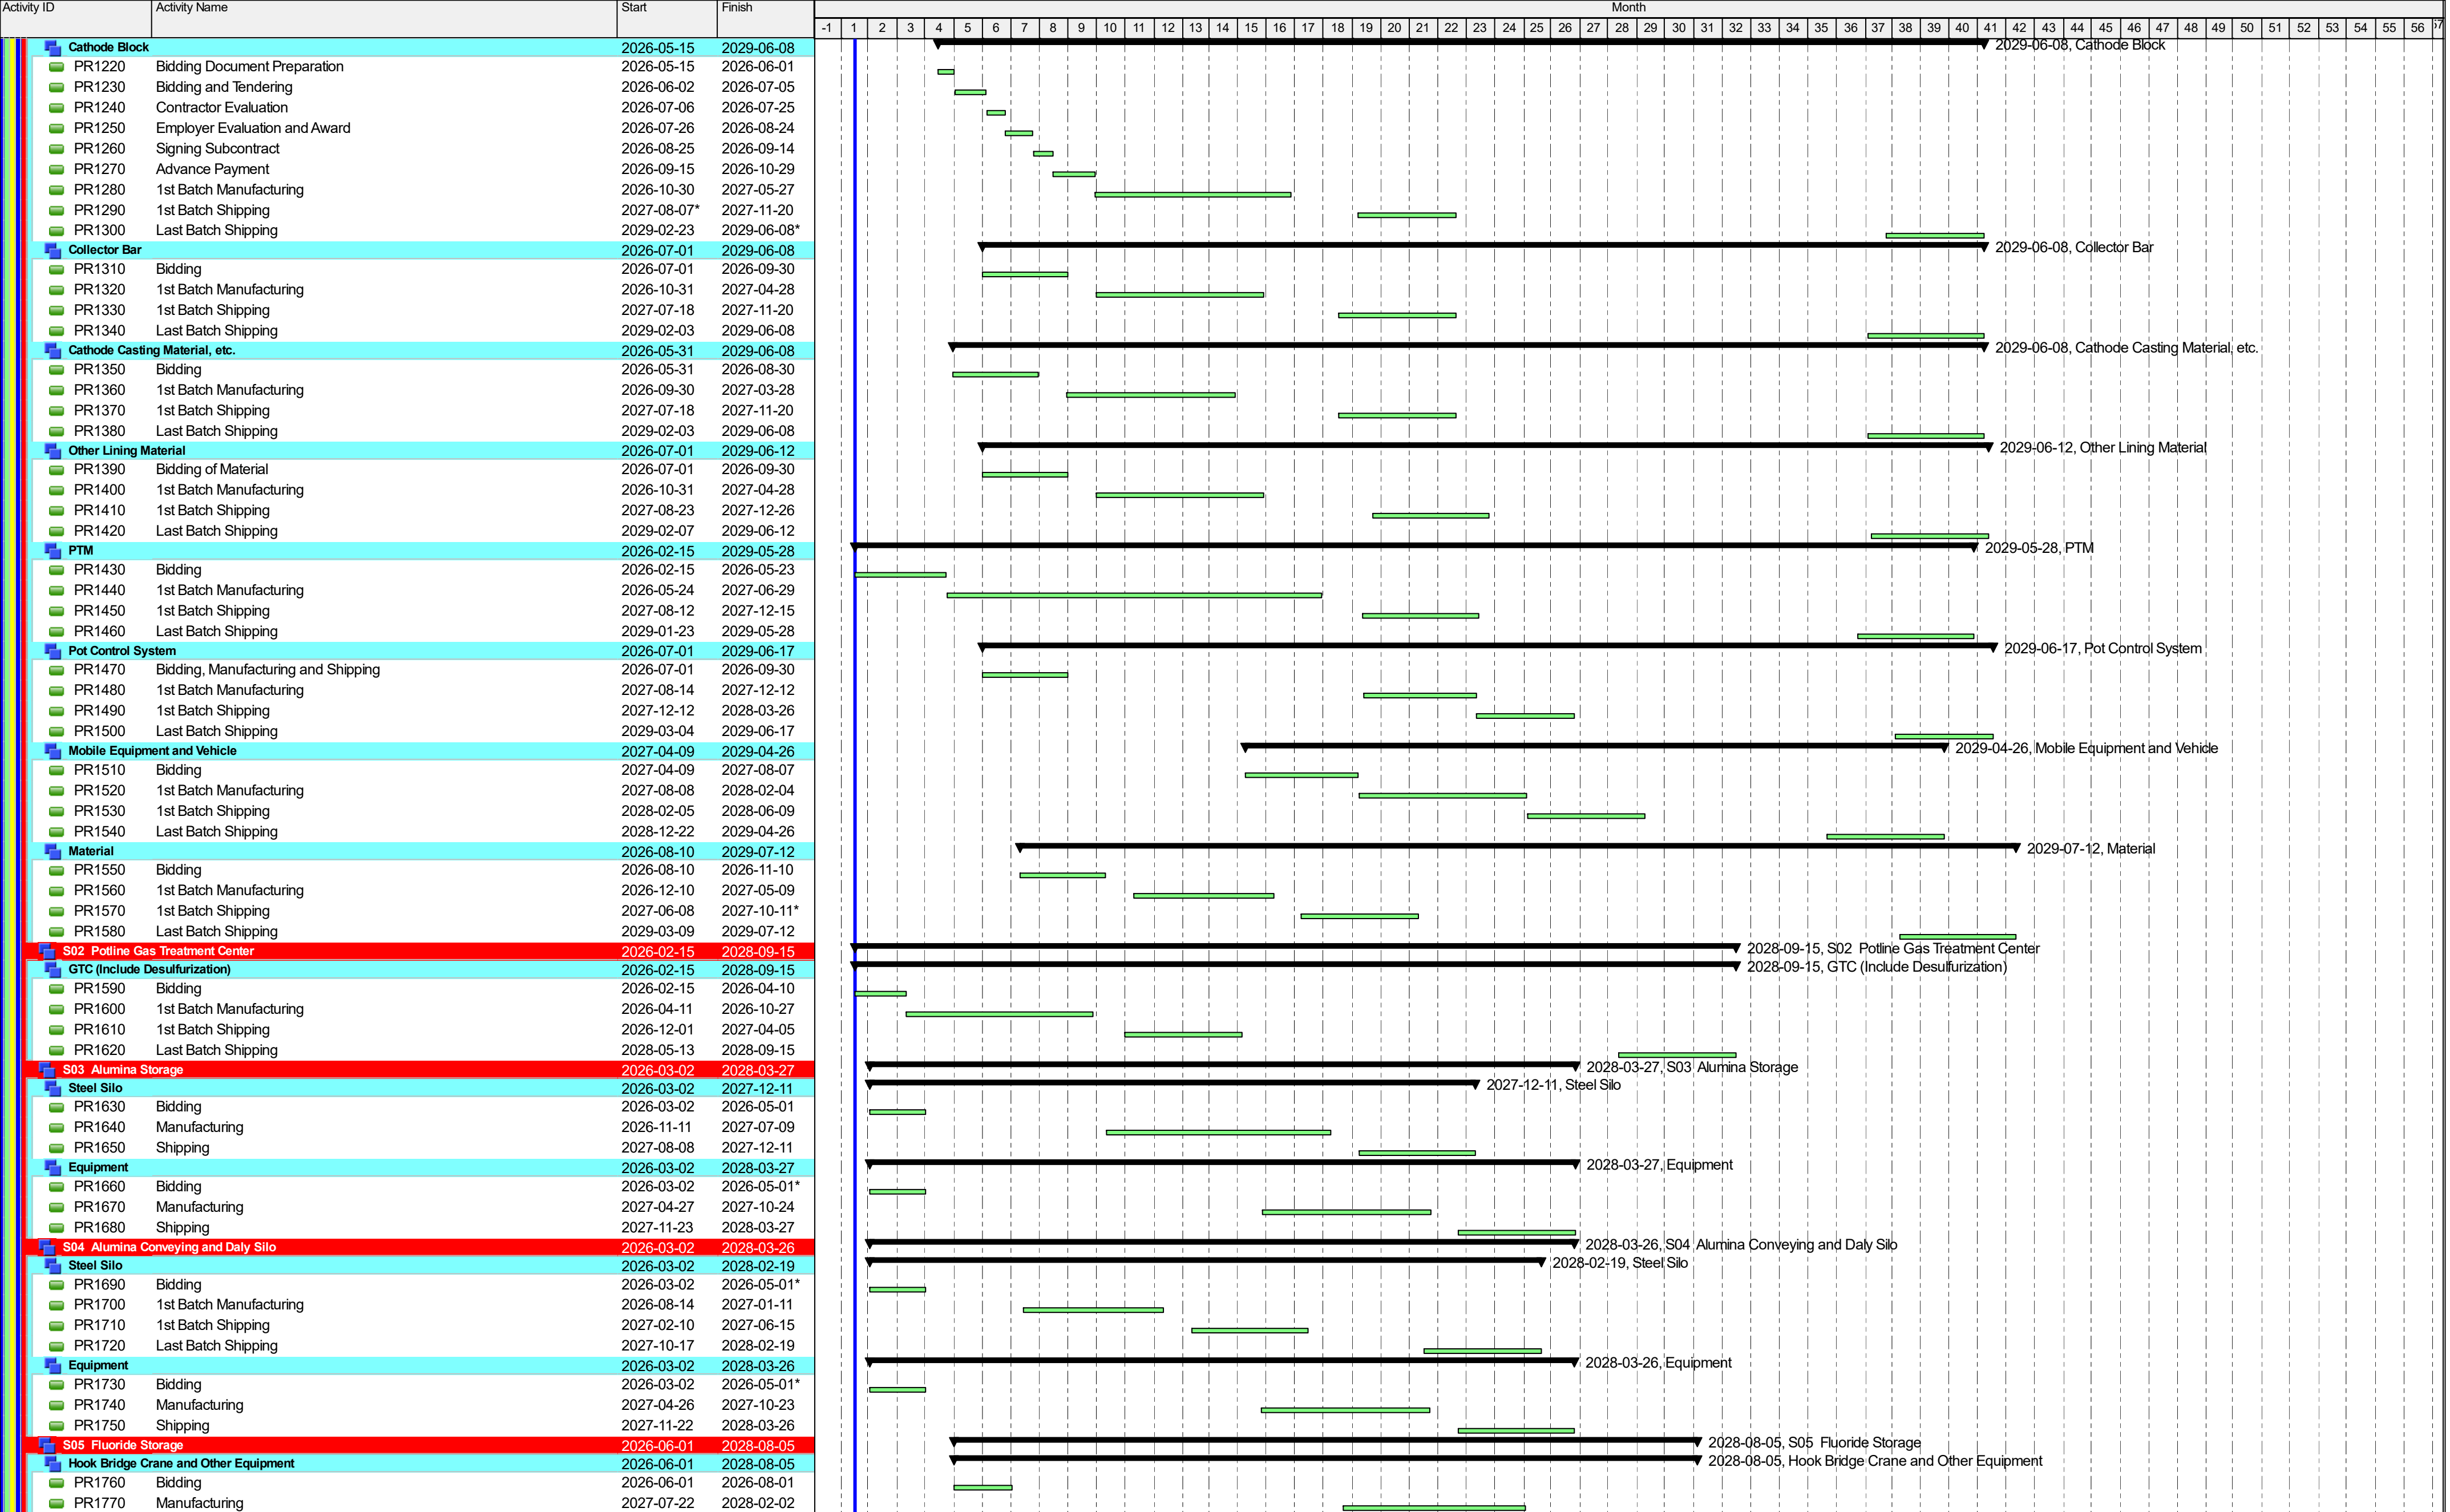



### Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
PR1780	Shipping	2028-04-02	2028-08-05
S06	Super Dense Phase Conveying System	2026-03-02	2029-07-14
Steel Silo		2026-03-02	2028-03-26
PR1790	Bidding	2026-03-02	2026-05-01*
PR1800	1st Batch Manufacturing	2026-07-05	2026-12-02
PR1810	1st Batch Shipping	2027-01-01	2027-05-06
PR1820	Last Batch Shipping	2027-11-22	2028-03-26
Equipment		2026-05-15	2029-07-14
PR1830	Bidding	2026-05-15	2026-07-15
PR1840	1st Batch Manufacturing	2026-12-25	2027-04-29
PR1850	1st Batch Shipping	2027-05-29	2027-09-30*
PR1860	Last Batch Shipping	2029-03-12	2029-07-14*
S07	Anode Covering Material Storage & Conveying System	2026-05-15	2028-04-15
Equipment and Material		2026-05-15	2028-04-15
PR1870	Bidding	2026-05-15	2026-07-15
PR1880	1st Batch Manufacturing	2026-09-28	2027-01-27
PR1890	1st Batch Shipping	2027-01-27	2027-06-01
PR1900	Last Batch Shipping	2027-12-12	2028-04-15
S08	Cast House	2026-03-15	2028-05-20
Gas Mixing Furnace		2026-03-15	2028-05-20
PR1910	Bidding	2026-03-15	2026-05-14
PR1920	Manufacturing	2027-03-22	2027-12-17
PR1930	Shipping	2028-01-16	2028-05-20
25kg Ingot Casting Machine		2026-03-15	2028-05-20
PR1940	Bidding	2026-03-15	2026-05-14*
PR1950	Manufacturing	2027-05-21	2027-12-17
PR1960	Shipping	2028-01-16*	2028-05-20
Hook Bridge Crane		2026-06-01	2028-03-20
PR1970	Bidding	2026-06-01	2026-08-01
PR1980	Manufacturing	2027-03-21	2027-10-17
PR1990	Shipping	2027-11-16	2028-03-20
S09	Crucible Cleaning Workshop	2026-04-12	2028-04-15
Hook Bridge Crane		2026-06-01	2028-04-15
PR2000	Bidding	2026-06-01	2026-08-01*
PR2010	Manufacturing	2027-06-15	2027-11-12
PR2020	Shipping	2027-12-12	2028-04-15
Crucible Cleaning Equipment		2026-04-12	2028-04-15
PR2030	Bidding	2026-04-12	2026-06-12
PR2040	Manufacturing	2027-02-15	2027-11-12
PR2050	Shipping	2027-12-12	2028-04-15
S11	Carbon Deposit Treatment Workshop	2026-04-12	2028-07-11
Single Beam Crane		2026-06-01	2028-07-11
PR2120	Bidding	2026-06-01	2026-08-01*
PR2130	Manufacturing	2027-09-10	2028-02-07
PR2140	Shipping	2028-03-08	2028-07-11
Carbon Deposit Treatment Equipment		2026-04-12	2028-07-11
PR2150	Bidding	2026-04-12	2026-06-12
PR2160	Manufacturing	2027-07-22	2028-02-07
PR2170	Shipping	2028-03-08*	2028-07-11
S10	Dross Treatment Workshop	2026-03-15	2028-08-16
Hook Bridge Crane		2026-06-01	2028-08-16
PR2060	Bidding	2026-06-01	2026-08-01*
PR2070	Manufacturing	2027-10-16	2028-03-14
PR2080	Shipping	2028-04-13	2028-08-16
Dross Treatment Equipment		2026-03-15	2028-08-16
PR2090	Bidding	2026-03-15	2026-06-12*
PR2100	Manufacturing	2027-07-18	2028-03-14
PR2110	Shipping	2028-04-13	2028-08-16
S13	SPL Temporary Storage	2026-06-01	2028-09-10
Hook Bridge Crane		2026-06-01	2028-09-10
PR2180	Bidding	2026-06-01	2026-08-01*
PR2190	Manufacturing	2027-11-10	2028-04-08
PR2200	Shipping	2028-05-08	2028-09-10
A00	Anode Plant	2026-02-15	2029-01-05
A01	GPC Storage and Conveying	2026-02-15	2028-02-04
Hook Bridge Crahe		2026-05-30	2028-02-04
PR2210	Bidding	2026-05-30	2026-07-29*
PR2220	Manufacturing	2027-02-19	2027-09-02
PR2230	Shipping	2027-10-02	2028-02-04
Other Equipment		2026-02-15	2028-02-04
PR2240	Bidding	2026-02-15	2026-04-16
PR2250	Manufacturing	2027-03-06	2027-09-02
PR2260	Shipping	2027-10-02	2028-02-04
A02	Calcination Shop	2026-03-30	2028-02-20
Equipment (Steel Structure, Conveyor, Feeder, Bucket Elevator, Crusher, etc.)		2026-03-30	2028-01-20

Remaining Level of Effort

Actual Work

Critical Remaining Work

summary


Actual Level of Effort

Remaining Work

Milestone

Page 7 of 28

## Project Schedule(Level 3)

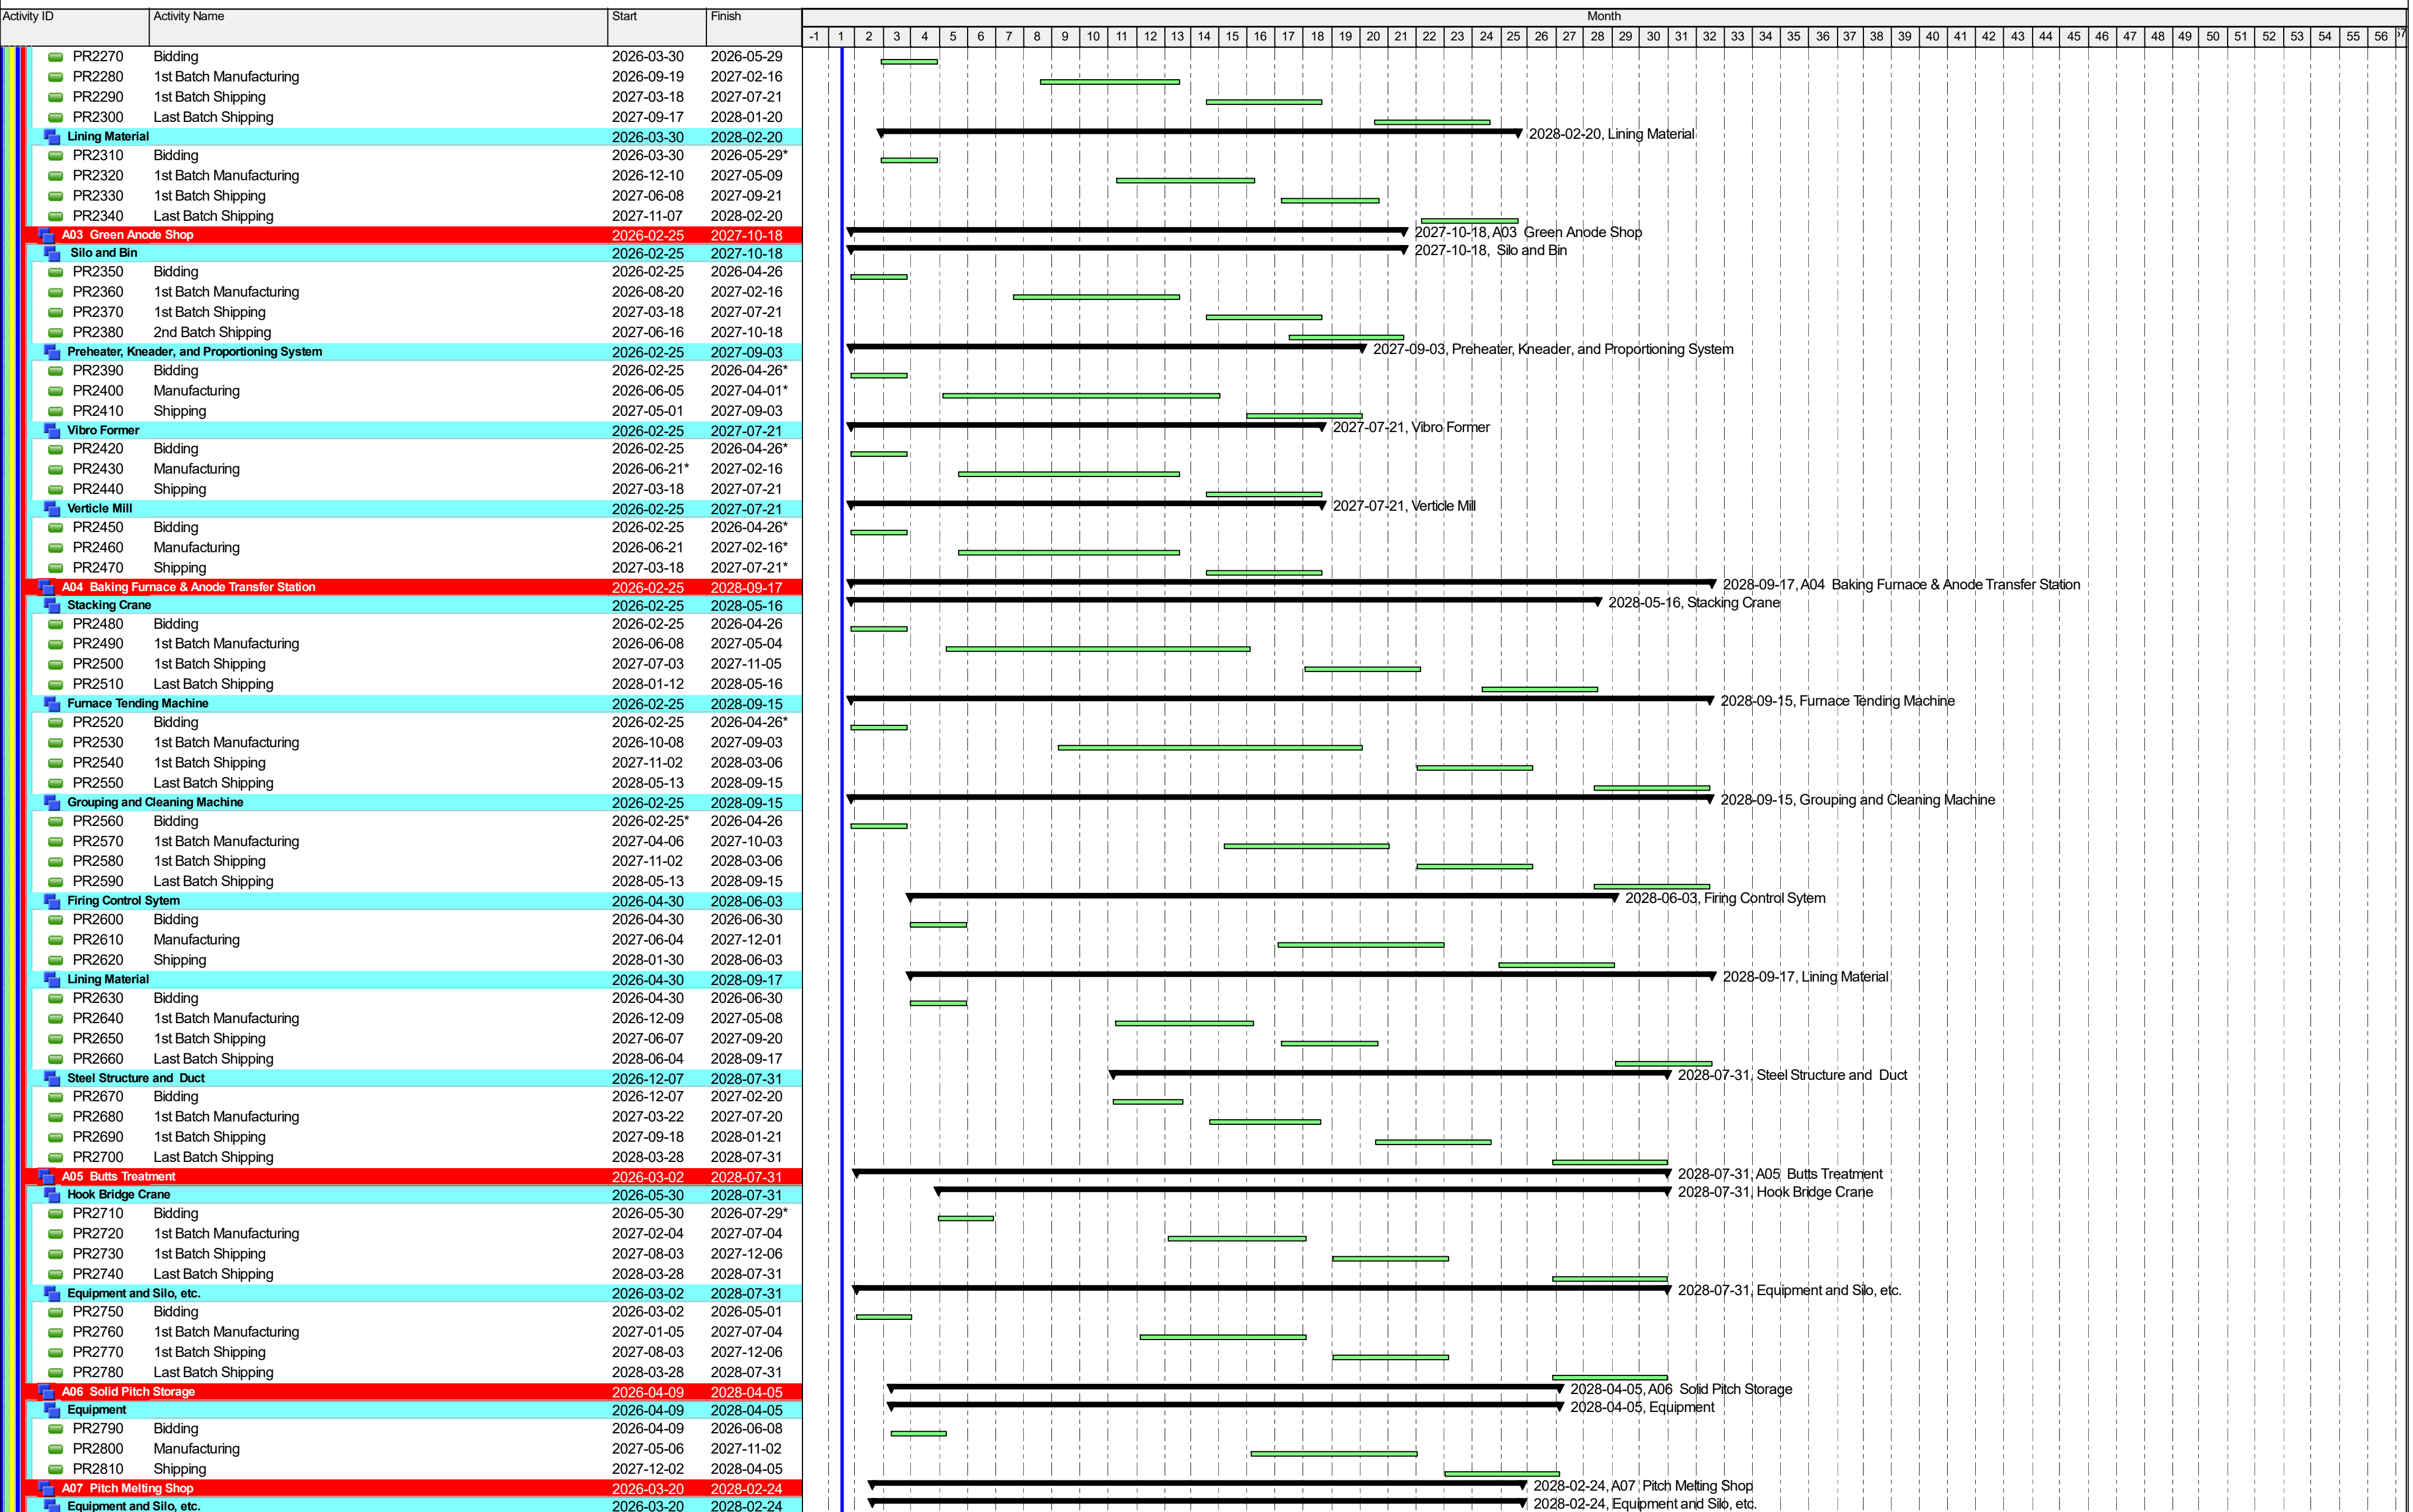



Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
	<div><div></div>PR2820Bidding</div>	2026-03-20	2026-05-19
	<div><div></div>PR2830Manufacturing</div>	2027-02-24	2027-09-22
	<div><div></div>PR2840Shipping</div>	2027-10-22	2028-02-24
A08	Baking Furnace Fume Treatment Center	2026-02-15	2029-01-05
	Equipment and Material	2026-02-15	2029-01-05
	<div><div></div>PR2850Bidding</div>	2026-02-15	2026-04-10*
	<div><div></div>PR28601st Batch Manufacturing</div>	2026-11-27	2027-08-04
	<div><div></div>PR28701st Batch Shipping</div>	2027-09-03	2028-01-06
	<div><div></div>PR28802nd Batch Shipping</div>	2028-09-02	2029-01-05
A09	Calcination Fume Treatment Center	2026-02-15	2027-11-20
	Equipment and Material	2026-02-15	2027-11-20
	<div><div></div>PR2890Bidding</div>	2026-02-15	2026-04-10
	<div><div></div>PR2900Manufacturing</div>	2026-10-11	2027-06-18
	<div><div></div>PR2910Shipping</div>	2027-07-18	2027-11-20
A10	Anode Rodding Shop	2026-03-02	2028-09-30
	Overhead Bridge Crane	2026-06-01	2028-09-30
	<div><div></div>PR2920Bidding</div>	2026-06-01	2026-08-01*
	<div><div></div>PR29301st Batch Manufacturing</div>	2027-03-01	2027-07-29
	<div><div></div>PR29401st Batch Shipping</div>	2027-08-28	2027-12-31
	<div><div></div>PR29502nd Batch Shipping</div>	2028-05-28	2028-09-30
	Frequency Induction Furnace	2026-03-02	2028-09-15
	<div><div></div>PR2960Bidding</div>	2026-03-02	2026-05-01
	<div><div></div>PR29701st Batch Manufacturing</div>	2026-12-15	2027-06-13
	<div><div></div>PR29801st Batch Shipping</div>	2027-07-13*	2027-11-15
	<div><div></div>PR29902nd Batch Shipping</div>	2028-05-13	2028-09-15
	Other Equipment and Material	2026-03-02	2028-09-30
	<div><div></div>PR3000Bidding</div>	2026-03-02	2026-05-01
	<div><div></div>PR30101st Batch Manufacturing</div>	2026-06-02	2027-03-29
	<div><div></div>PR30201st Batch Shipping</div>	2027-04-28	2027-08-31
	<div><div></div>PR3030Last Batch Shipping</div>	2028-05-28	2028-09-30
A11	Bath Treatment System	2026-03-02	2028-06-30
	Equipment	2026-03-02	2028-06-30
	<div><div></div>PR3040Bidding</div>	2026-03-02	2026-05-01
	<div><div></div>PR30501st Batch Manufacturing</div>	2027-01-31	2027-10-28
	<div><div></div>PR30601st Batch Shipping</div>	2027-11-27	2028-03-31
	<div><div></div>PR30702nd Batch Shipping</div>	2028-02-26	2028-06-30
A12	Stem and Stub Repair Workshop	2026-03-30	2028-09-15
	Equipment	2026-03-30	2028-09-15
	<div><div></div>PR3080Bidding</div>	2026-03-30	2026-05-29
	<div><div></div>PR30901st Batch Manufacturing</div>	2027-08-31	2028-02-27
	<div><div></div>PR31001st Batch Shipping</div>	2028-03-28	2028-07-31
	<div><div></div>PR31102nd Batch Shipping</div>	2028-05-13	2028-09-15
A13	Waste Heat Boiler Room	2026-03-30	2027-11-05
	Equipment	2026-03-30	2027-11-05
	<div><div></div>PR3120Bidding</div>	2026-03-30	2026-05-29
	<div><div></div>PR3130Manufacturing</div>	2026-09-06	2027-06-03
	<div><div></div>PR3140Shipping</div>	2027-07-03	2027-11-05
A14	Heat Transfer Medium Boiler and Pump Room	2026-03-30	2028-02-04
	Equipment	2026-03-30	2028-02-04
	<div><div></div>PR3150Bidding</div>	2026-03-30	2026-05-29
	<div><div></div>PR3160Manufacturing</div>	2026-12-06	2027-09-02
	<div><div></div>PR3170Shipping</div>	2027-10-02	2028-02-04
U00	Utilities	2026-03-02	2029-06-17
U01	330kV Power Distribution Device	2026-03-02	2028-07-06
	Incoming and Feeder Equipment, etc.	2026-03-02	2028-07-06
	<div><div></div>PR3180Bidding</div>	2026-03-02	2026-05-01
	<div><div></div>PR31901st Batch Manufacturing</div>	2026-12-22	2027-07-20
	<div><div></div>PR32001st Batch Shipping</div>	2027-08-19	2027-12-22
	<div><div></div>PR32102nd Batch Shipping</div>	2028-03-03	2028-07-06
U02	330/10.5kV Substation and Center Control Room of the Smelter	2026-03-15	2028-07-31
	Transformer, Switchgear, etc.	2026-03-15	2028-07-31
	<div><div></div>PR3220Bidding</div>	2026-03-15	2026-05-14
	<div><div></div>PR32301st Batch Manufacturing</div>	2026-09-16	2027-05-14
	<div><div></div>PR32401st Batch Shipping</div>	2027-06-13	2027-10-16
	<div><div></div>PR32502nd Batch Shipping</div>	2028-03-28	2028-07-31
U03	Rectifier Station	2026-03-02	2028-09-20
	Rectifier & Transformer	2026-03-02	2028-09-20
	<div><div></div>PR3260Bidding</div>	2026-03-02	2026-05-01
	<div><div></div>PR32701st Batch Manufacturing</div>	2026-05-02	2027-05-16
	<div><div></div>PR32801st Batch Shipping</div>	2027-07-08	2027-11-10
	<div><div></div>PR32902nd Batch Shipping</div>	2028-05-18	2028-09-20
	Capacitor and Harmonic Treatment Device	2026-05-02	2028-09-20

## Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
Month			
-1 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40 41 42 43 44 45 46 47 48 49 50 51 52 53 54 55 56 57			
PR3330	2nd Batch Shipping	2028-06-22	2028-09-20
U06	11kV Distribution Room in Anode Area	2026-04-14	2027-11-20
Equipment		2026-04-14	2027-11-20
PR3340	Bidding	2026-04-14	2026-06-15
PR3350	Manufacturing	2027-01-09	2027-07-08
PR3360	Shipping	2027-08-07	2027-11-20
U07	Diesel Generator Room	2026-05-15	2027-10-11
Equipment		2026-05-15	2027-10-11
PR3370	Bidding	2026-05-15	2026-07-14
PR3380	Manufacturing	2026-12-10	2027-05-09
PR3390	Shipping	2027-06-08	2027-10-11
U09	Compressor Station	2026-05-15	2027-11-06
Equipment		2026-05-15	2027-11-06
PR3400	Bidding	2026-05-15	2026-07-14*
PR3410	Manufacturing	2026-10-07	2027-06-04
PR3420	Shipping	2027-07-04	2027-11-06
U10	Water Supply Pressurized Pump House	2026-04-30	2027-12-31
Pump		2026-04-30	2027-12-31
PR3430	Bidding	2026-04-30	2026-06-29
PR3440	Manufacturing	2027-03-01	2027-07-29
PR3450	Shipping	2027-08-28	2027-12-31
Unit U11-U20		2026-05-30	2028-05-31
Pump, Cooling Tower, and Water Treatment Equipment		2026-05-30	2028-05-31
PR3460	1st Batch Bidding	2026-05-30	2026-08-29
PR3470	1st Batch Manufacturing	2027-02-28	2027-07-28
PR3480	1st Batch Shipping	2027-08-28	2027-12-31
PR3490	Last Batch Shipping	2028-01-27	2028-05-31
U22	Comprehensive Maintenance Workshop	2026-03-30	2028-06-25
Equipment		2026-03-30	2028-06-25
PR3500	Bidding	2026-03-30	2026-05-29
PR3510	Manufacturing	2027-07-26	2027-12-23*
PR3520	Shipping	2028-02-21	2028-06-25
U23	Pot Maintenance Shop	2026-03-02	2027-07-21
Equipment (Bridge Crane and Intermediate Frequency Furnace)		2026-03-02	2027-07-21
PR3530	Bidding	2026-03-02	2026-05-01
PR3540	Manufacturing	2026-05-02	2027-01-26
PR3550	Shipping	2027-03-18	2027-07-21
U24	Carbon Repair Room	2026-03-30	2028-05-06
Equipment		2026-03-30	2028-05-06
PR3560	Bidding	2026-03-30	2026-05-29
PR3570	Manufacturing	2027-07-26	2027-12-23
PR3580	Shipping	2028-01-02	2028-05-06*
U25	General Warehouse	2026-03-30	2027-10-17
Equipment		2026-03-30	2027-10-17
PR3590	Bidding	2026-03-30	2026-05-29
PR3600	Manufacturing	2026-12-16	2027-05-15
PR3610	Shipping	2027-06-14	2027-10-17
U27	Truck Scale	2026-06-30	2028-02-25
Equipment		2026-06-30	2028-02-25
PR3620	Bidding	2026-06-30	2026-08-29
PR3630	Manufacturing	2027-05-26	2027-09-23
PR3640	Shipping	2027-10-23	2028-02-25
U31	Piping and Cable Tray Network	2027-02-21	2029-06-17
Material		2027-02-21	2029-06-17
PR3650	Bidding	2027-02-21	2027-04-23
PR3660	1st Batch Manufacturing	2027-04-23	2027-07-22
PR3670	1st Batch Shipping	2027-07-23	2027-11-25
PR3680	Last Batch Shipping	2029-02-12	2029-06-17
U33	Natural Gas Press Regulating Station	2026-06-30	2028-04-20
Equipment		2026-06-30	2028-04-20
PR3690	Bidding	2026-06-30	2026-08-29
PR3700	Manufacturing	2027-05-21	2027-11-17
PR3710	Shipping	2027-12-17	2028-04-20
Process Material		2026-07-01	2029-06-17
PR3720	1st Batch Bidding	2026-07-01	2026-08-31
PR3730	1st Batch Manufacturing	2026-09-01	2026-11-30
PR3740	1st Batch Shipping	2026-12-01	2027-04-05
PR3750	Last Batch Shipping	2029-02-12	2029-06-17
Management and Welfare Facilities		2026-08-23	2028-02-14
Equipment and Material		2026-08-23	2028-02-14
PR3760	1st Batch Bidding	2026-08-23	2026-10-23
PR3770	1st Batch Manufacturing	2026-10-24	2027-02-21
PR3780	1st Batch Shipping	2027-03-23	2027-07-26
PR3790	2nd Batch Shipping	2027-10-12	2028-02-14
Soil Treatment Package by Employer		2026-04-14	2027-05-15

Remaining Level of Effort

Actual Work

Critical Remaining Work

summary

Actual Level of Effort


Remaining Work

Milestone


Page 10 of 28



Project Schedule(Level 3)

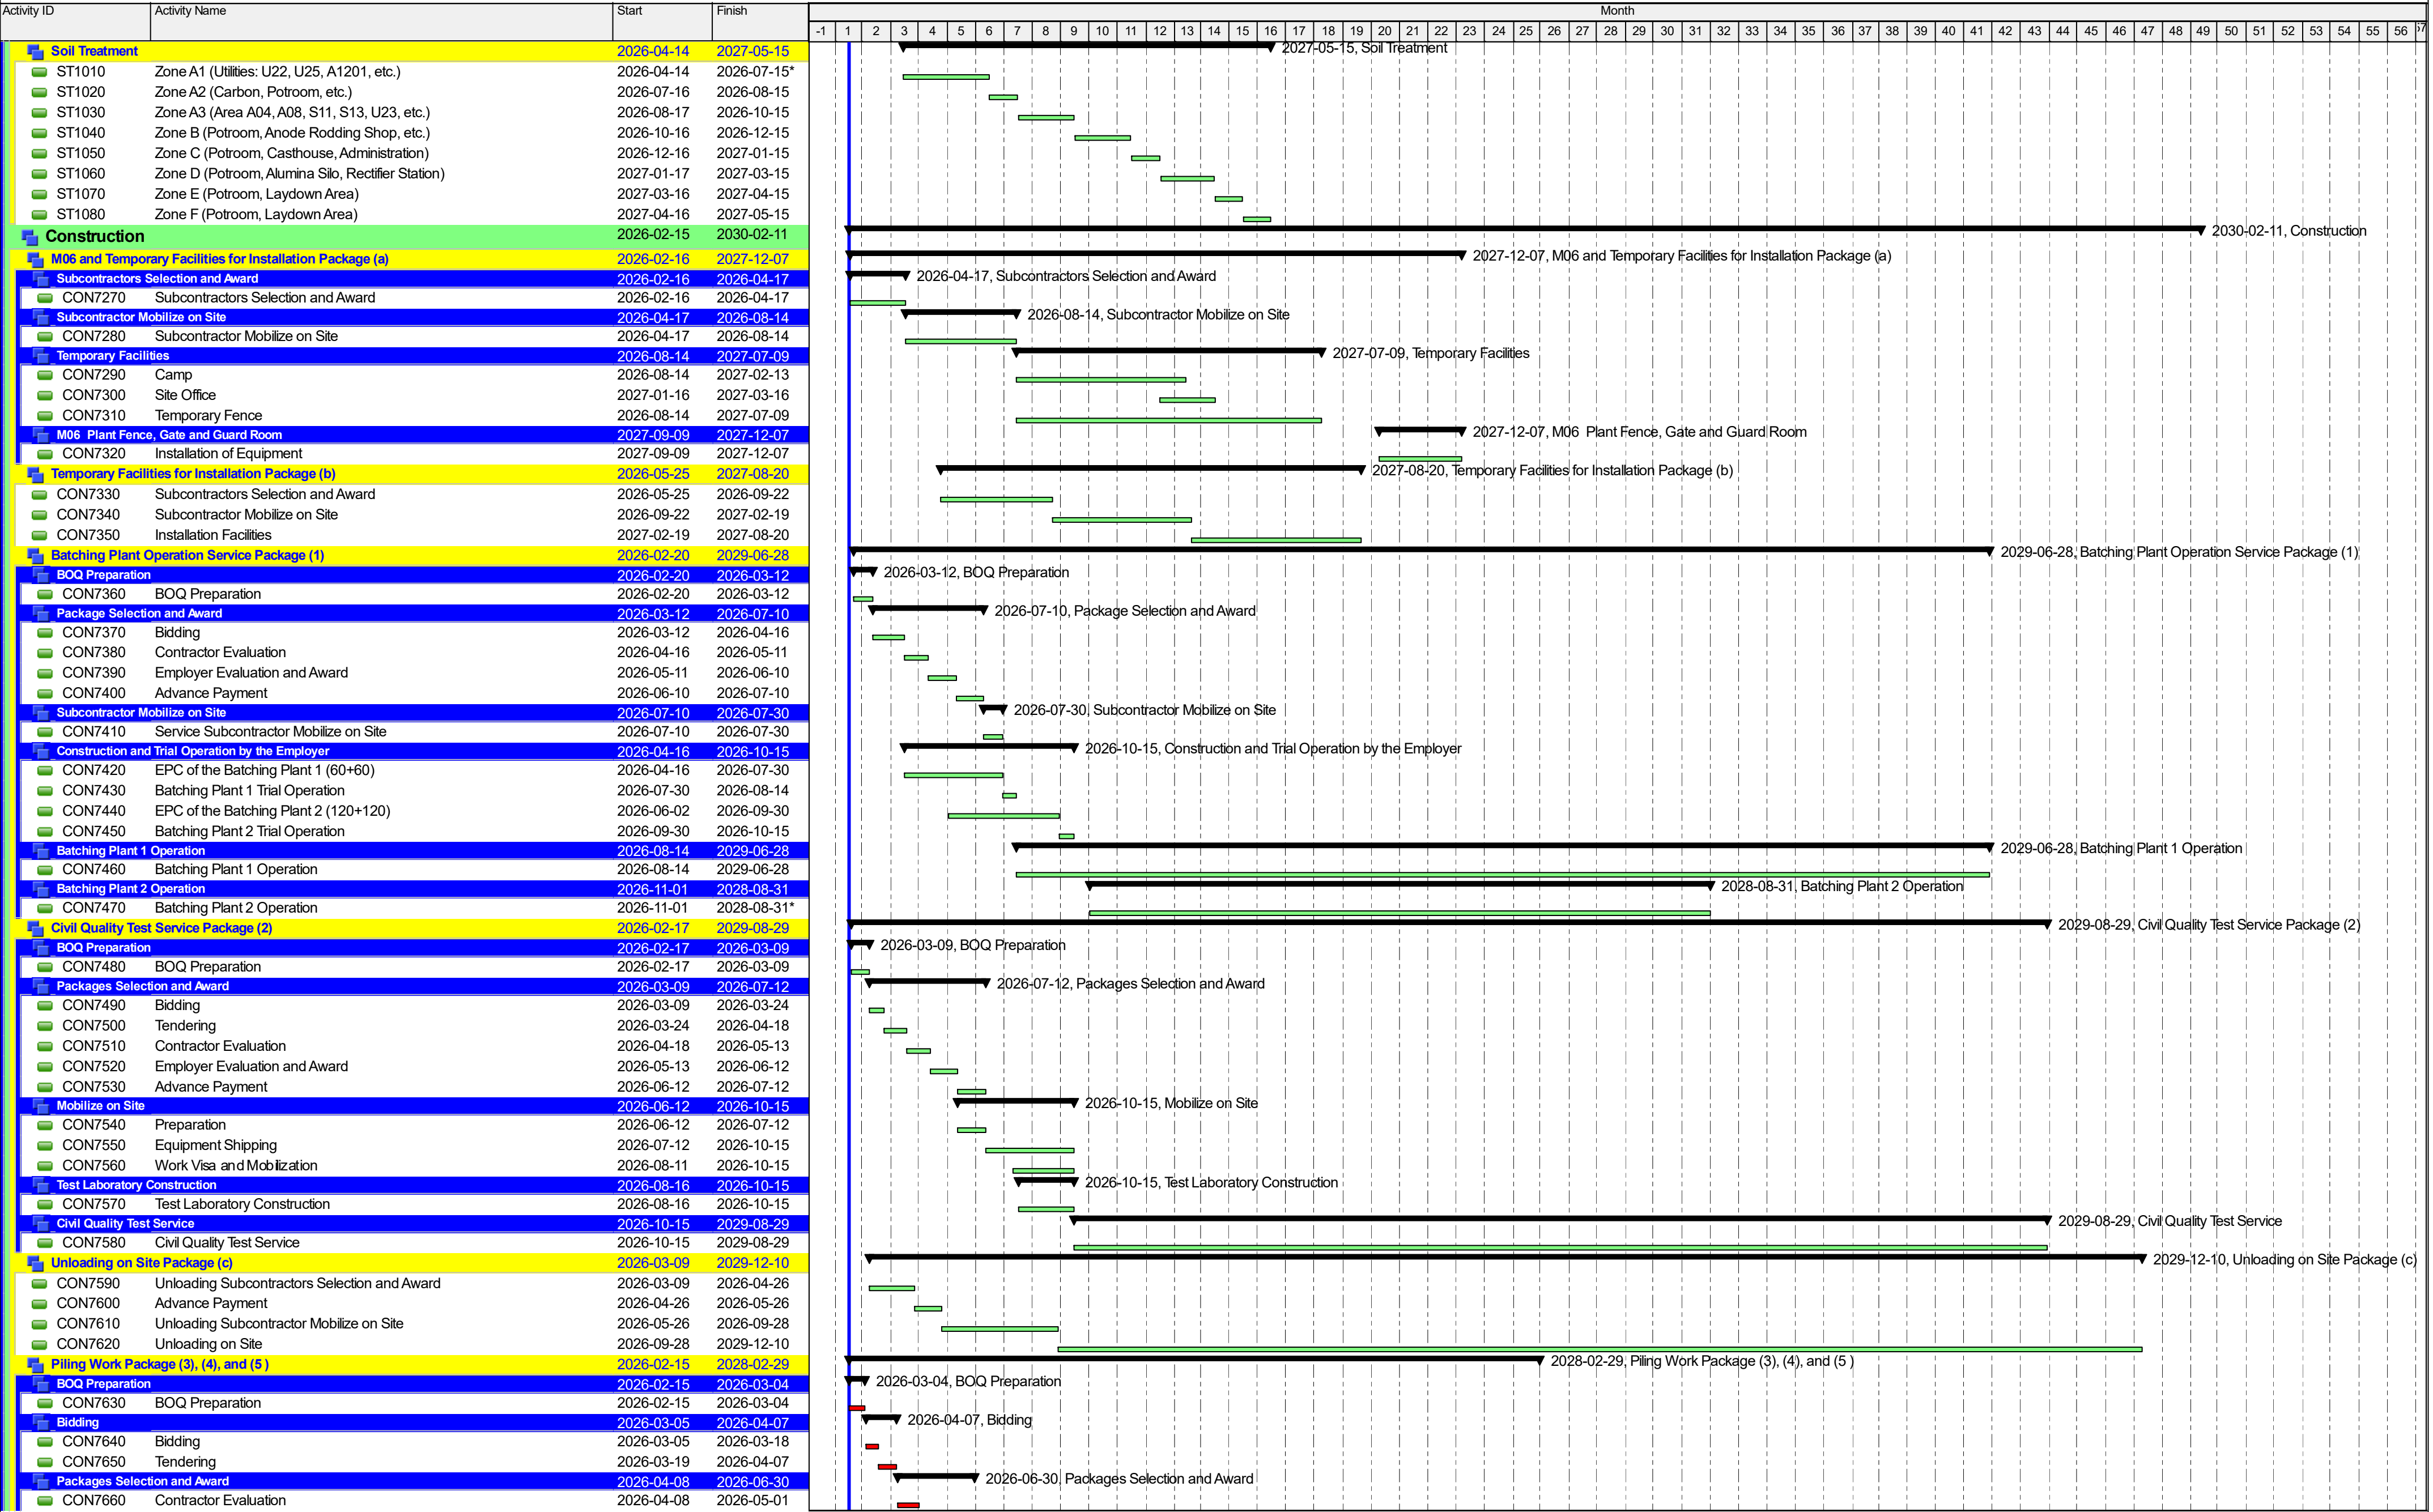

Project Schedule(Level 3)

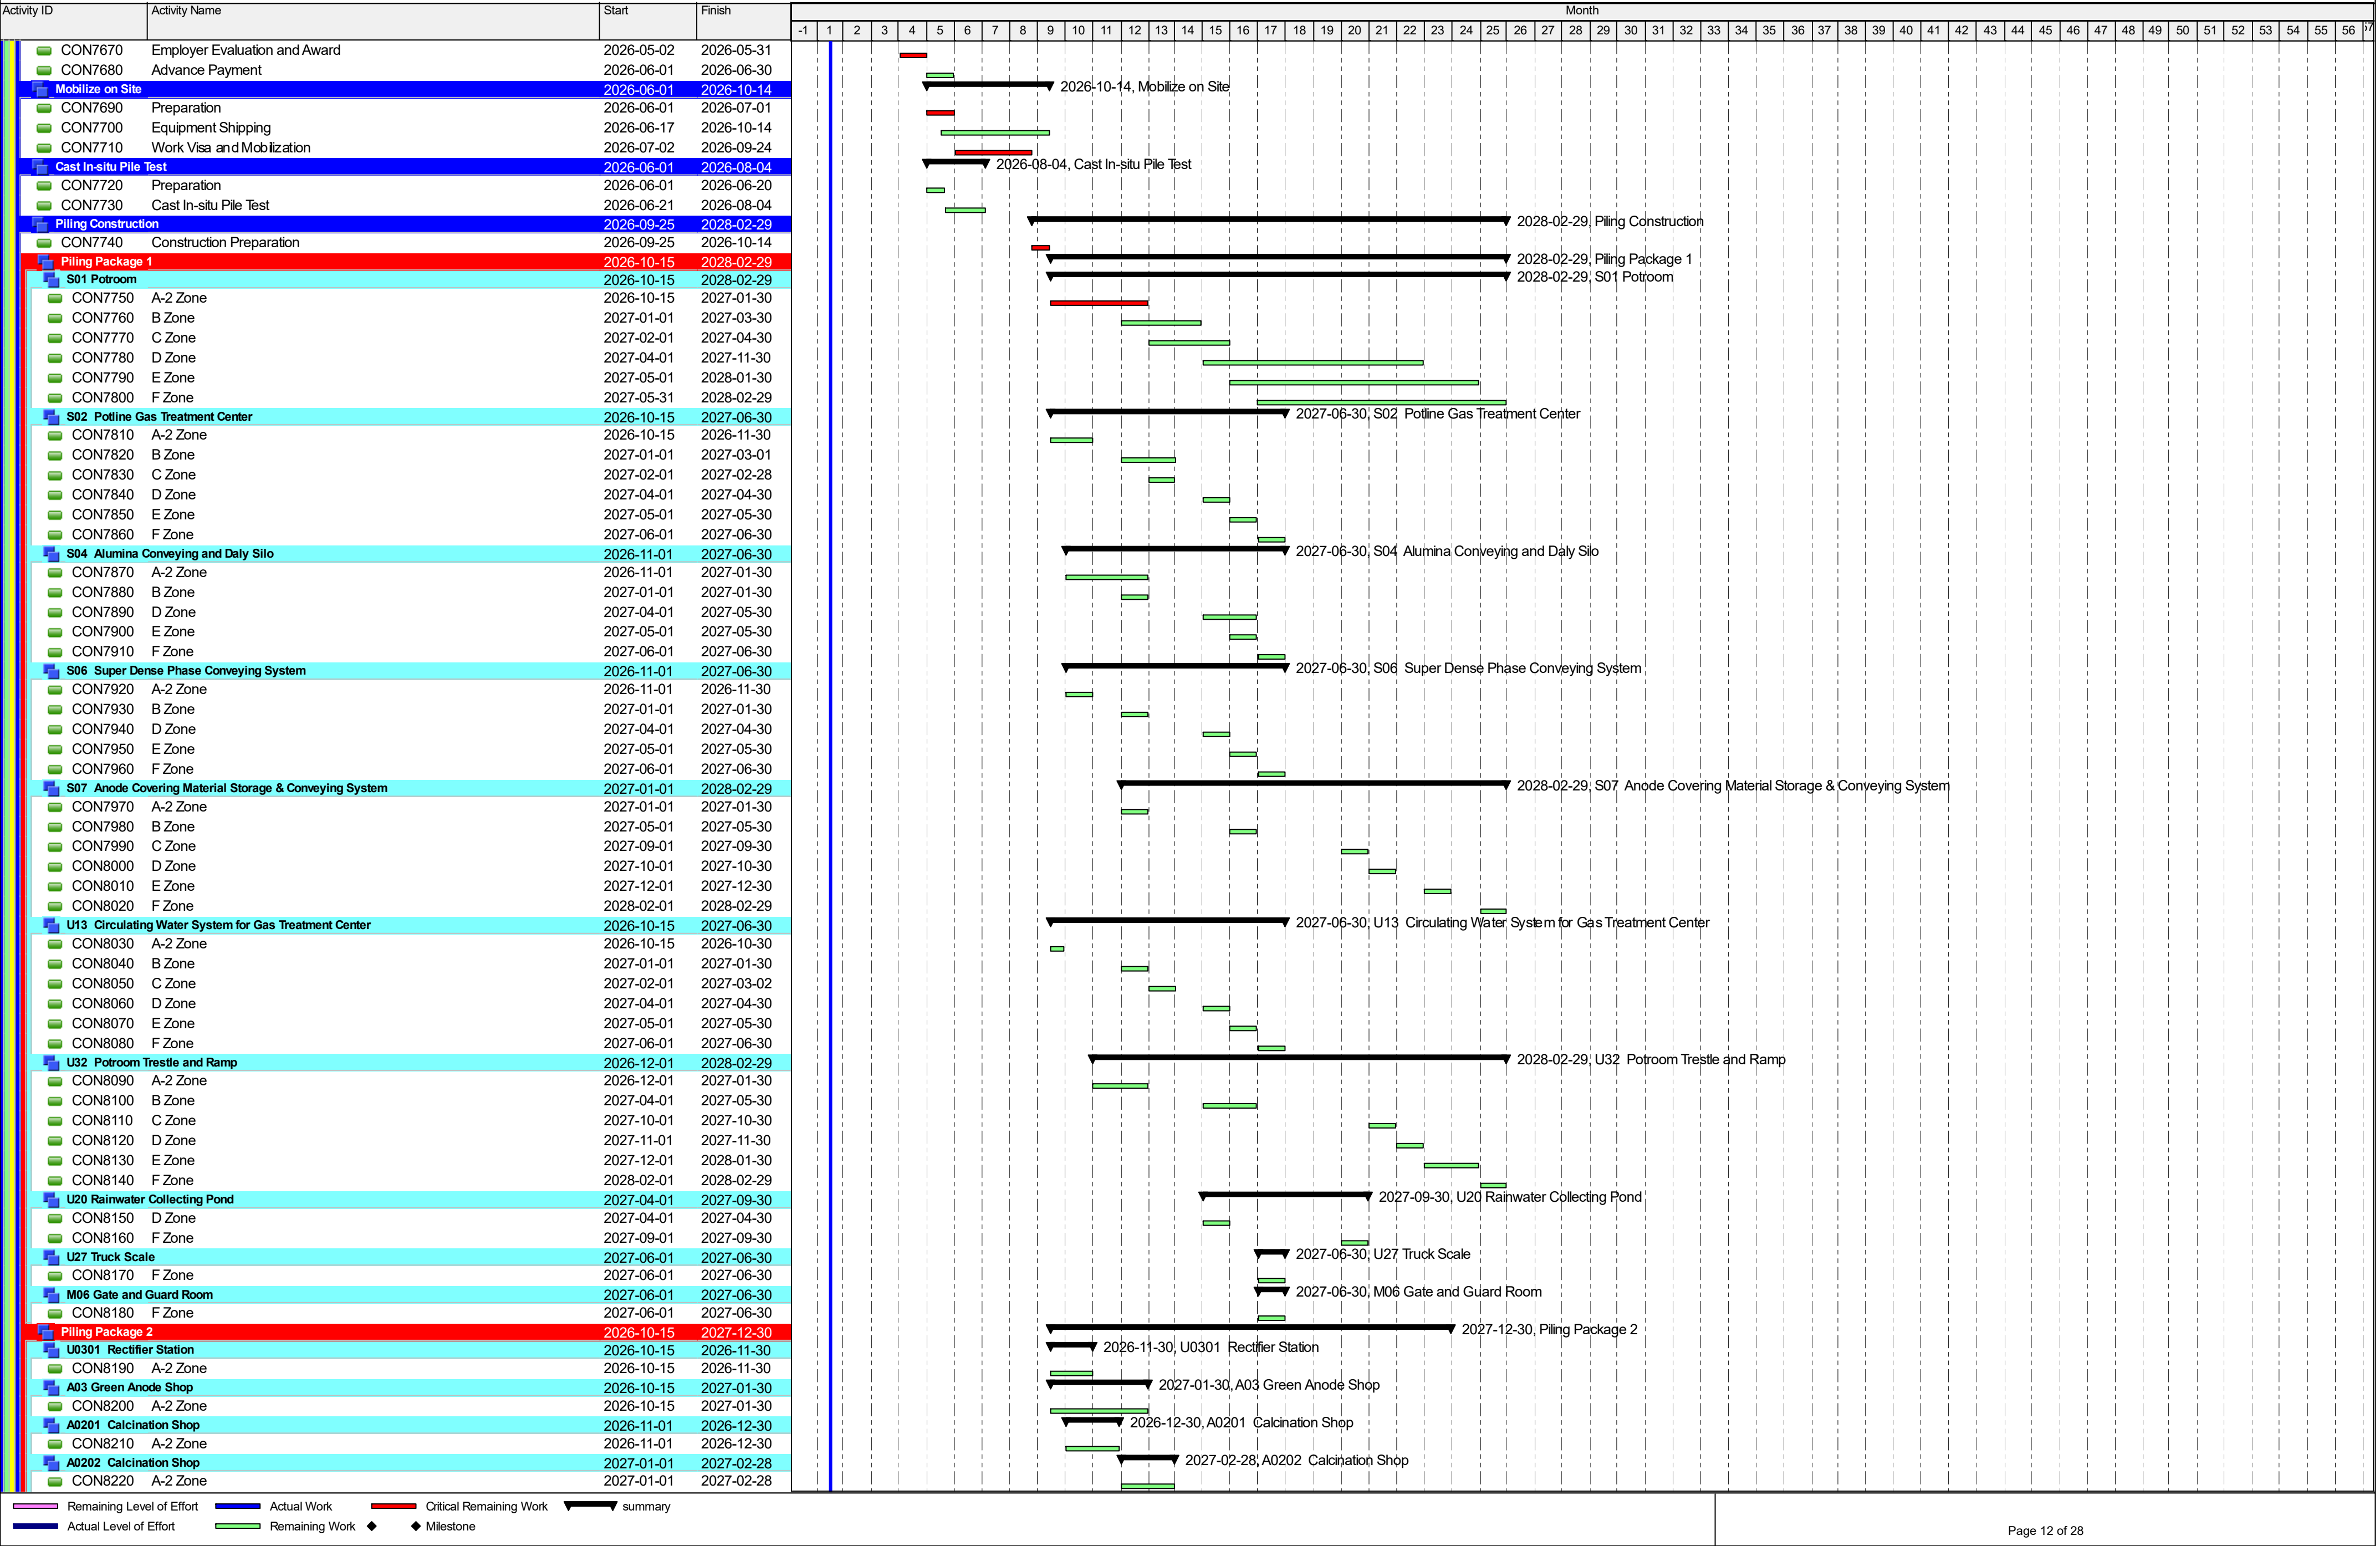

Page 12 of 28




Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
A01 GPC Storage and Conveying		2026-12-01	2027-02-28
CON8230 A-2 Zone		2026-12-01	2027-02-28
A06 Solid Pitch Storage		2027-01-01	2027-01-30
CON8240 A-2 Zone		2027-01-01	2027-01-30
A07 Pitch Melting Shop		2027-01-01	2027-02-28
CON8250 A-2 Zone		2027-01-01	2027-02-28
A09 Calcination Fume Treatment Center		2027-01-01	2027-02-28
CON8260 A-2 Zone		2027-01-01	2027-02-28
A14 Heat Transfer Medium Boiler and Pump Room		2027-02-01	2027-03-15
CON8270 A-2 Zone		2027-02-01	2027-03-15
A13, S05, U14, U24, U06, and U16		2027-03-01	2027-03-15
CON8280 A-2 Zone		2027-03-01	2027-03-15
A1001 Anode Rodding Shop		2026-10-15	2027-02-28
CON8290 A-2 Zone		2026-10-15	2027-02-28
A0501, A1101, and U15		2027-02-01	2027-02-28
CON8300 A-2 Zone		2027-02-01	2027-02-28
E01 Raw Material Conveying system		2027-03-01	2027-06-30
CON8310 D Zone		2027-03-01	2027-06-30
S03 Alumina Storage		2027-04-01	2027-06-30
CON8320 D Zone		2027-04-01	2027-06-30
U0101 330kV Power Distribution Device		2027-04-01	2027-06-30
CON8330 D Zone		2027-04-01	2027-06-30
U0201 330/10.5kV Substation and Center Control Room		2027-04-01	2027-05-30
CON8340 D Zone		2027-04-01	2027-05-30
U26 and M06		2027-04-01	2027-04-30
CON8350 D Zone		2027-04-01	2027-04-30
U05 Emergency Oil Pools and Oil Storage Facilities		2027-05-01	2027-05-30
CON8360 D Zone		2027-05-01	2027-05-30
U0102 330kV Power Distribution Device		2027-07-01	2027-12-30
CON8370 D Zone		2027-07-01	2027-12-30
U0202 330/10.5kV Substation and Center Control Room		2027-07-01	2027-12-30
CON8380 D Zone		2027-07-01	2027-12-30
U0302 Rectifier Station		2027-07-01	2027-12-30
CON8390 D Zone		2027-07-01	2027-12-30
A1201, U22, and U25		2027-02-01	2027-03-15
CON8400 A-1 Zone		2027-02-01	2027-03-15
U10 and U18		2027-03-01	2027-05-30
CON8410 A-1 Zone		2027-03-01	2027-05-30
U19 and U26		2027-03-01	2027-06-30
CON8420 A-1 Zone		2027-03-01	2027-06-30
Piling Package 3		2026-11-15	2027-09-30
U23 Reduction Pot Repair Room		2026-11-15	2027-02-28
CON8430 A-3 Zone		2026-11-15	2027-02-28
A0401 Baking Furnace & Anode Transfer Station		2026-11-15	2027-03-30
CON8440 A-3 Zone		2026-11-15	2027-03-30
A08 Baking Furnace Fume Treatment Center		2026-11-15	2027-04-30
CON8450 A-3 Zone		2026-11-15	2027-04-30
A0402 Baking Furnace & Anode Transfer Station		2027-04-01	2027-09-30
CON8460 A-3 Zone		2027-04-01	2027-09-30
S11 and S13		2027-02-01	2027-03-30
CON8470 A-3 Zone		2027-02-01*	2027-03-30
A1002 Anode Rodding Shop		2027-01-01	2027-09-30
CON8480 B Zone		2027-01-01	2027-09-30
A0502, U09, U11, U12, and A1102		2027-04-01	2027-05-30
CON8490 B Zone		2027-04-01	2027-05-30
M06 Gate and Guard Room		2027-02-01	2027-03-02
CON8510 C Zone		2027-02-01	2027-03-02
S08 Cast House		2027-04-01	2027-09-30
CON8520 C Zone		2027-04-01	2027-09-30
A1202 Stem and Stub Repair Workshop		2027-04-01	2027-05-30
CON8530 C Zone		2027-04-01	2027-05-30
S09 and S10		2027-05-01	2027-06-30
CON8540 C Zone		2027-05-01	2027-06-30
M01, M02, M03, and M04		2027-05-01	2027-09-30
CON8550 C Zone		2027-05-01	2027-09-30
S00 Aluminum Reduction Plant Civil Work Package (6) and (7)		2026-03-12	2028-09-08
BOQ Preparation		2026-03-12	2026-04-13
CON8560 BOQ Preparation		2026-03-12	2026-04-13
Bidding		2026-04-14	2026-06-08
CON8570 Bidding		2026-04-14	2026-05-04
CON8580 Tendering and Bid Clarification Meeting		2026-05-05	2026-06-08
Civil Subcontractors Selection and Award		2026-06-09	2026-09-24
CON8590 Contractor Evaluation		2026-06-09	2026-07-09
CON8600 Employer Evaluation and Award		2026-07-09	2026-08-08
CON8610 Advance Payment		2026-08-09	2026-09-24
Civil Subcontractor Mobilize on Site		2026-09-25	2027-01-24
CON8620 Civil Subcontractor Mobilize on Site		2026-09-25	2027-01-24


<

## Project Schedule(Level 3)

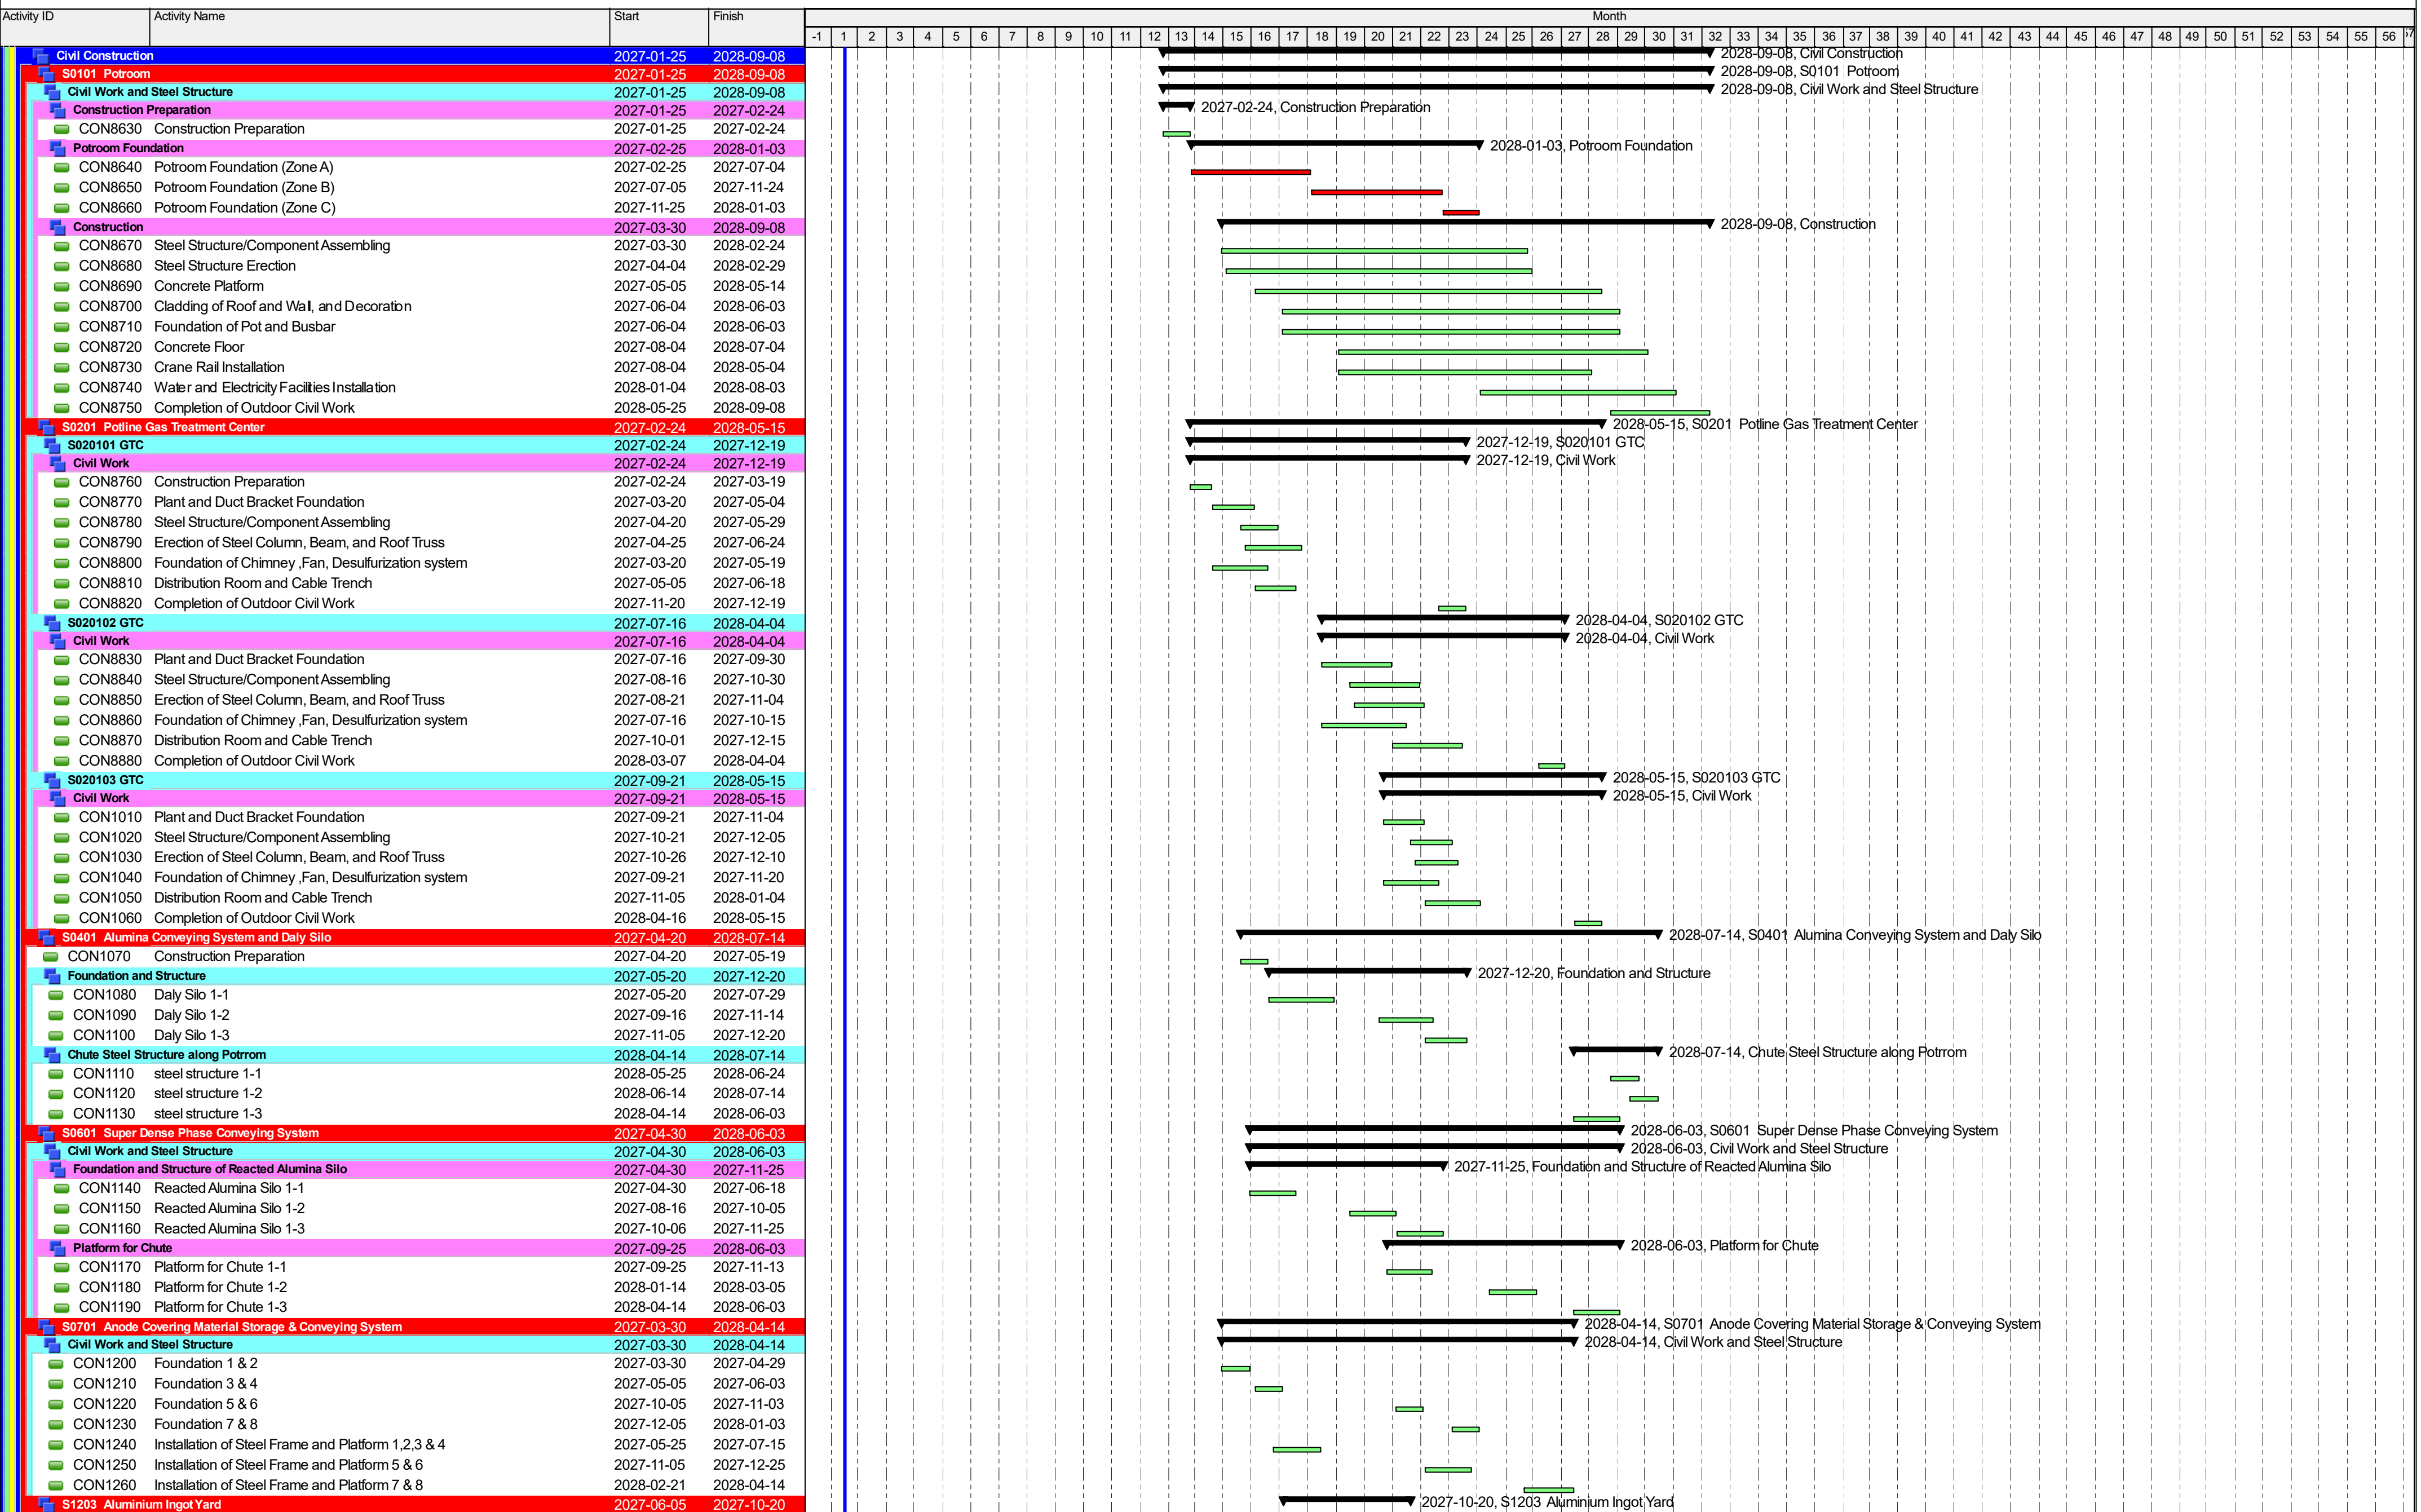



Project Schedule(Level 3)	
---------------------------	--

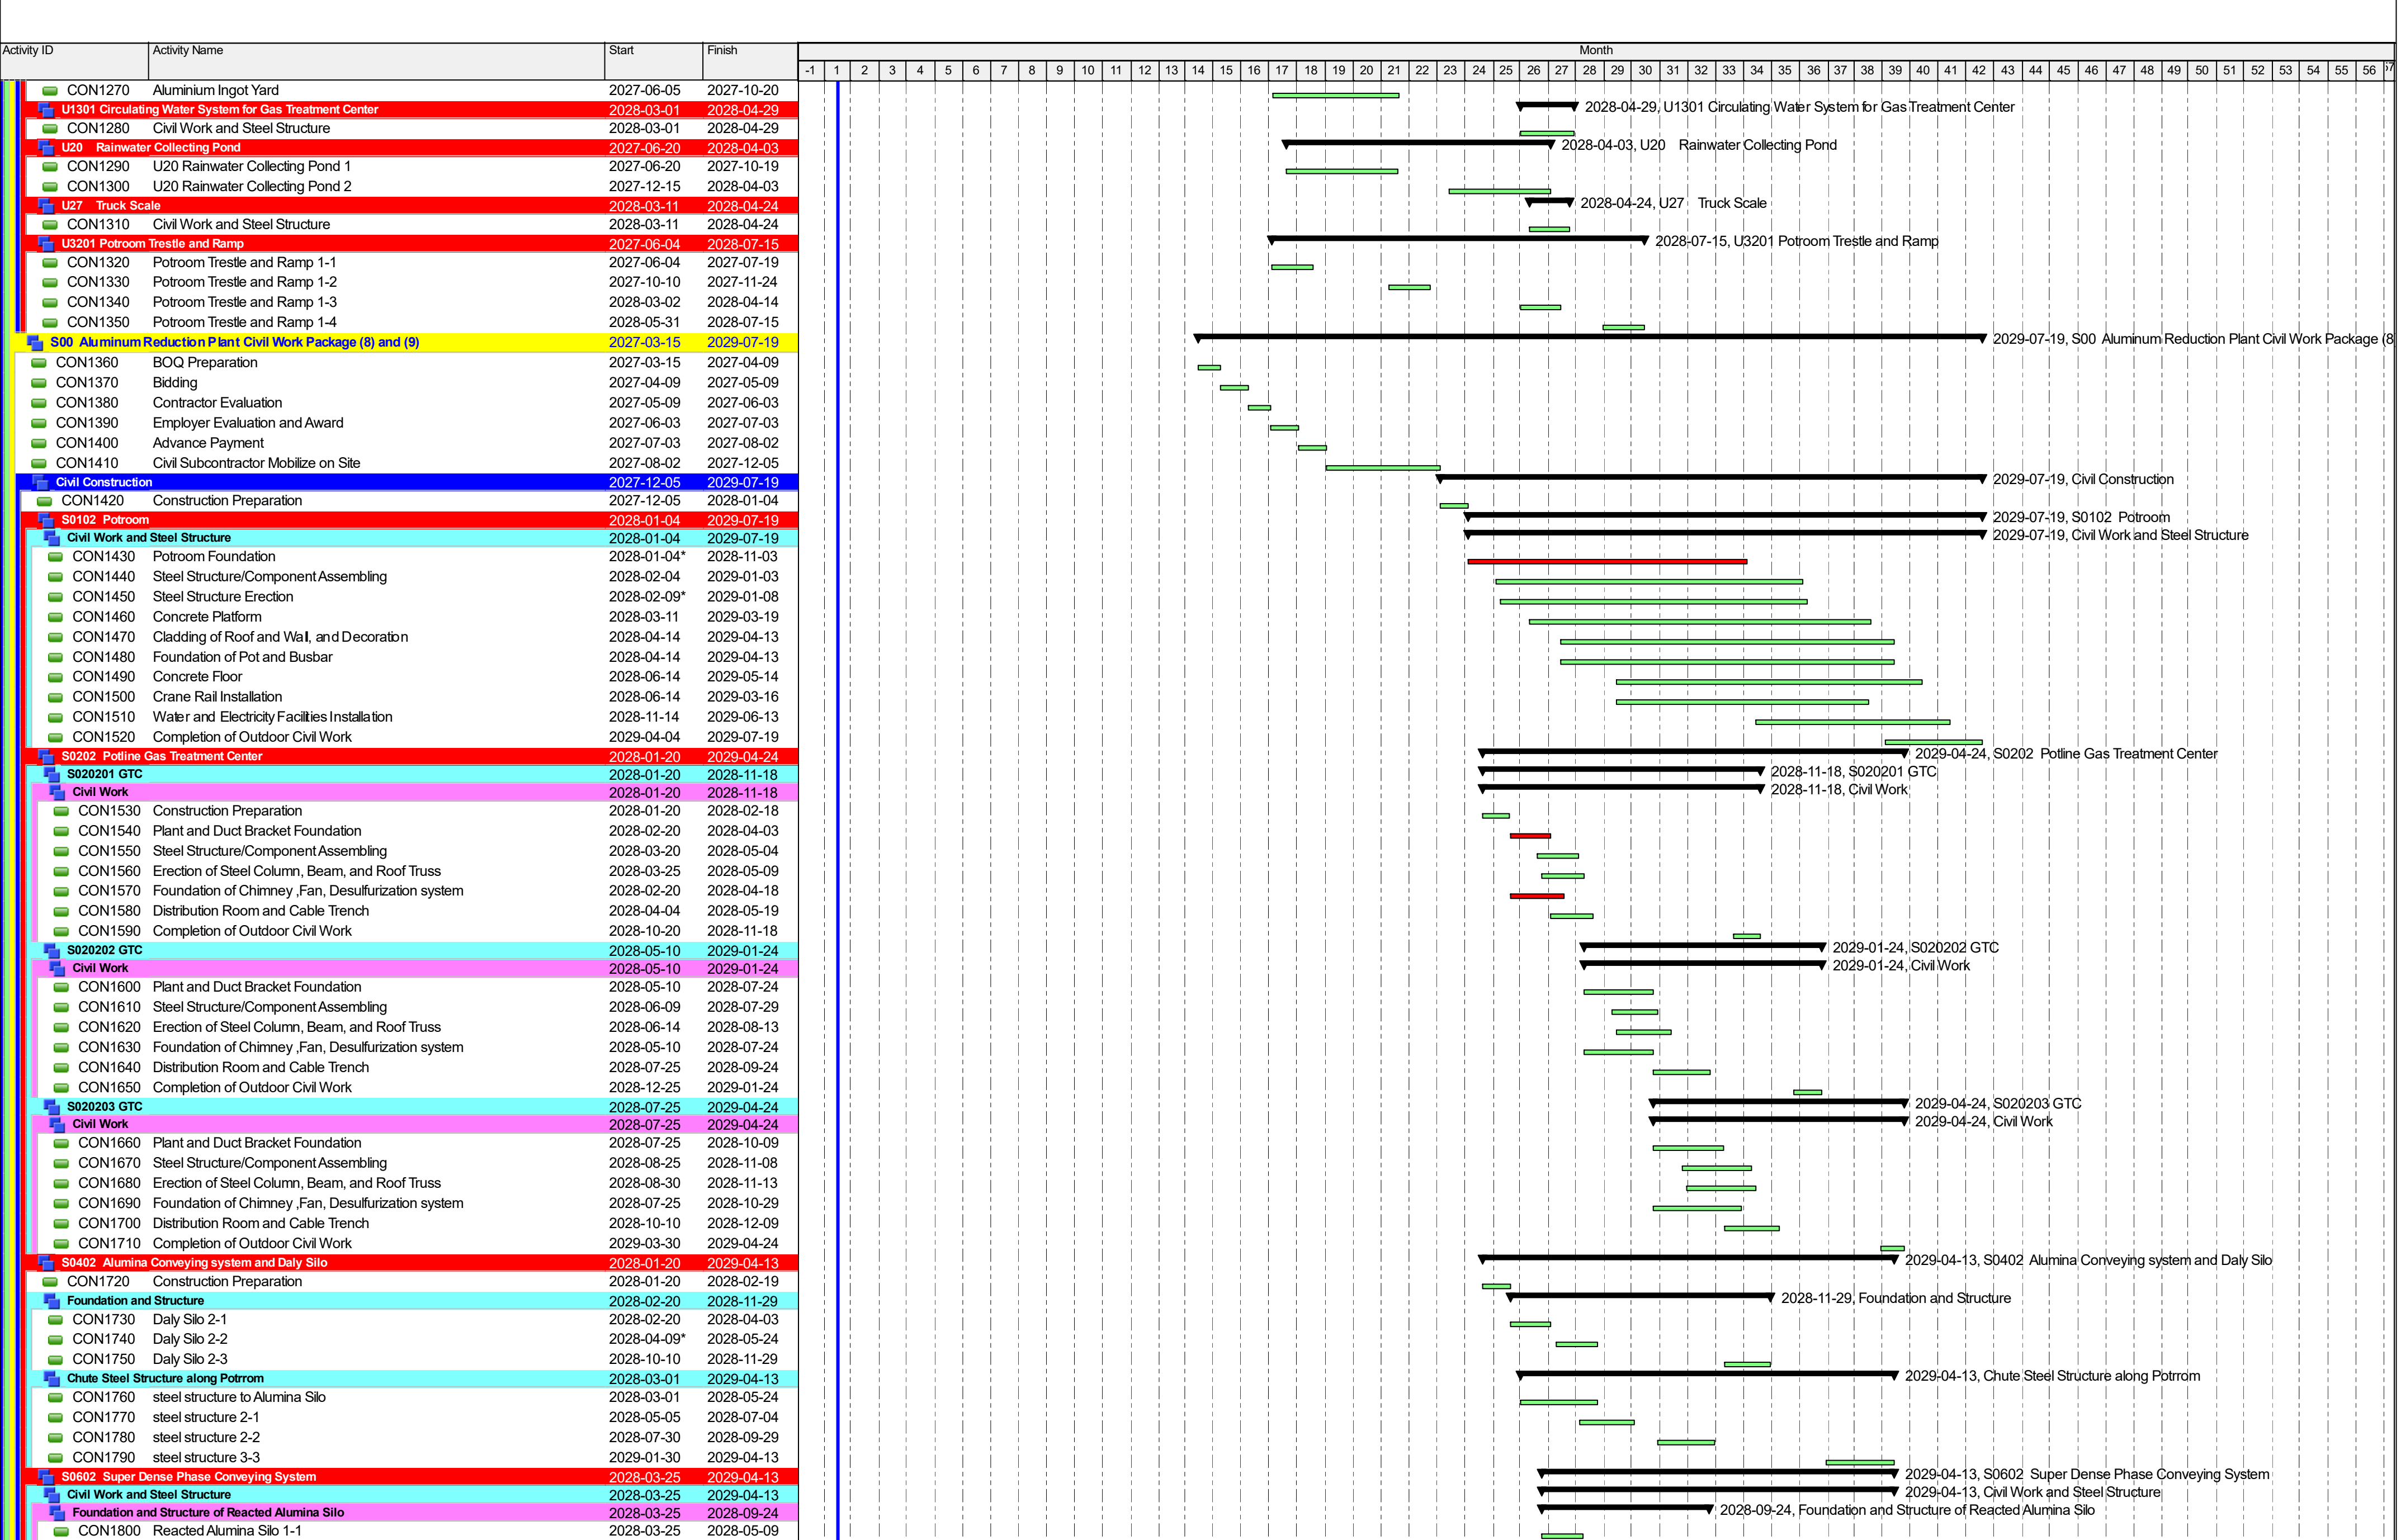

Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
S0702	Anode Covering Material Storage & Conveying System	2028-02-04	2029-02-24
Civil Work and Steel Structure		2028-02-04	2029-02-24
CON1860	Foundation 1 & 2	2028-02-04	2028-03-05
CON1870	Foundation 3 & 4	2028-03-25	2028-04-24
CON1880	Foundation 5 & 6	2028-08-14	2028-09-24
CON1890	Foundation 7 & 8	2028-10-10	2028-11-08
CON1900	Installation of Steel Frame and Platform 1,2,3 & 4	2028-04-04	2028-05-29
CON1910	Installation of Steel Frame and Platform 5 & 6	2028-09-25	2028-11-08
CON1920	Installation of Steel Frame and Platform 7 & 8	2029-01-20	2029-02-24
U1302	Circulating Water System for Gas Treatment Center	2029-01-09	2029-03-11
Civil Work and Steel Structure		2029-01-09	2029-03-11
U3202	Potroom Trestle and Ramp	2028-04-14	2029-06-13
CON1940	Potroom Trestle and Ramp 2-1	2028-04-14	2028-05-29
CON1950	Potroom Trestle and Ramp 2-2	2028-09-09	2028-10-24
CON1960	Potroom Trestle and Ramp 2-3	2029-01-14	2029-03-01
CON1970	Potroom Trestle and Ramp 2-4	2029-04-30	2029-06-13
S00	Aluminum Reduction Plant (Potroom, SDPC, ACMS) Installation Package (d) and (e)	2026-07-26	2030-02-11
CON1980	Installation Subcontractors Selection and Award	2026-07-26	2026-10-24
CON1990	Advance Payment	2026-10-24	2026-12-08
CON2000	Installation Subcontractor Mobilize on Site	2026-12-08	2027-05-07
Mechanical and E&I Installation		2027-07-15	2030-02-11
S0101	Potroom	2027-10-05	2029-03-31
CON2010	Installation Temporary Overhead Crane	2027-10-05	2028-02-03
Installation		2027-10-20	2029-03-31
CON2020	Busbar Fixture Fabrication	2027-10-20	2027-11-09
CON2030	Busbar Pre-assembling in Workshop	2027-11-09	2027-11-24
CON2040	Busbar	2027-11-25	2028-08-24
CON2050	Pot shell	2028-01-09	2028-09-24
CON2060	Pot Lining	2028-02-09	2028-11-08
CON2070	Superstructure	2028-03-11	2028-12-09
CON2080	PTM	2028-02-13	2028-11-13
CON2090	PTM Test	2028-04-13	2029-01-13
CON2100	Pot Control System	2028-05-10	2028-12-14
CON2110	No Load Interlocking Test	2028-08-09	2029-03-15
CON2120	Issue Phase 1AMC Certificate	2029-03-31	2029-03-31
S0102	Potroom	2028-08-14	2030-02-11
CON2130	Installation Temporary Overhead Crane	2028-08-14	2028-12-14
Installation		2028-10-25	2030-02-11
CON2140	Busbar	2028-10-25	2029-07-24
CON2150	Pot shell	2028-12-10	2029-08-24
CON2160	Pot Lining	2029-01-09	2029-10-09
CON2170	Superstructure	2029-02-09	2029-11-08
CON2180	PTM	2028-12-25	2029-09-24
CON2190	Pot Control System	2029-04-09	2029-11-13
CON2200	No Load Interlocking Test	2029-06-25	2030-02-05
CON2210	Issue Phase 1B MC Certificate	2030-02-11	2030-02-11
S0601	Super Dense Phase Conveying System (without reacted silo)	2027-11-14	2028-12-14
Installation		2027-11-14	2028-12-14
Main Chute and Air Pipe		2027-11-14	2028-07-19
CON2220	Main Chute and Air Pipe 1-1	2027-11-14	2027-12-29
CON2230	Main Chute and Air Pipe 1-2	2028-03-06	2028-04-18
CON2240	Main Chute and Air Pipe 1-3	2028-06-04	2028-07-19
Fan, Electrical Equipment and Instrumentation		2027-11-14	2028-08-03
CON2250	MEI 1-1	2027-11-14	2028-01-13
CON2260	MEI 1-2	2028-03-06	2028-05-04
CON2270	MEI 1-2	2028-06-04	2028-08-03
Installation		2028-02-14	2028-12-14
CON2280	Chute on Superstructure	2028-05-15	2028-12-14
CON2290	No Load Test	2028-02-14	2028-11-14
S0602	Super Dense Phase Conveying System (without reacted silo)	2028-09-14	2029-11-13
Installation		2028-09-14	2029-11-13
Main Chute and Air Pipe		2028-09-14	2029-05-29
CON2300	Main Chute and Air Pipe 2-1	2028-09-14	2028-11-18
CON2310	Main Chute and Air Pipe 2-2	2028-12-20	2029-02-03
CON2320	Main Chute and Air Pipe 2-3	2029-04-14	2029-05-29
Fan, Electrical Equipment and Instrumentation		2028-09-14	2029-06-13
CON2330	MEI 1-1	2028-09-14	2028-11-13
CON2340	MEI 1-2	2028-12-20	2029-02-18
CON2350	MEI 1-3	2029-04-14	2029-06-13

Remaining Level of Effort

Actual Work

Critical Remaining Work

summary

Actual Level of Effort

Remaining Work

Milestone

Page 16 of 28



# Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
<b>Installation</b> 2028-12-15 2029-11-13			
CON2360	Chute on Superstructure	2029-04-20	2029-11-13
CON2370	No Load Test	2028-12-15	2029-10-14
<b>S0701 Anode Covering Material Storage &amp; Conveying System</b> 2027-07-15 2028-05-30			
<b>Installation</b> 2027-07-15 2028-05-30			
CON2380	High Level Silo 1,2,3 & 4	2027-07-15	2027-08-18
CON2390	High Level Silo 5 & 6	2027-12-26	2028-01-09
CON2400	High Level Silo 7 & 8	2028-04-16	2028-04-30
CON2410	Bucket Lifting Equipment 1,2,3 & 4	2027-08-20	2027-10-09
CON2420	Bucket Lifting Equipment 5 & 6	2028-01-10	2028-03-01
CON2430	Bucket Lifting Equipment 7 & 8	2028-05-01	2028-05-30
<b>S0702 Anode Covering Material Storage &amp; Conveying System</b> 2028-05-30 2029-04-29			
<b>Installation</b> 2028-05-30 2029-04-29			
CON2440	High Level Silo 1,2,3 & 4	2028-05-30	2028-07-04
CON2450	High Level Silo 5 & 6	2028-11-09	2028-11-24
CON2460	High Level Silo 7 & 8	2029-02-25	2029-03-16
CON2470	Bucket Lifting Equipment 1,2,3 & 4	2028-07-05	2028-09-08
CON2480	Bucket Lifting Equipment 5 & 6	2028-11-25	2029-01-13
CON2490	Bucket Lifting Equipment 7 & 8	2029-03-17	2029-04-29
<b>S1203 Aluminium Ingot Yard</b> 2027-10-21 2027-11-10			
<b>Installation (Cabling and Lighting)</b> 2027-10-21 2027-11-10			
<b>U20 Rainwater Collecting Pond (pump, etc.)</b> 2027-10-20 2028-04-23			
<b>CON2510 Installation Pond 1 (Pump and Cabling)</b> 2027-10-20 2027-11-08			
<b>CON2520 Installation Pond 2 (Pump and Cabling)</b> 2028-04-04 2028-04-23			
<b>U27 Truck Scale</b> 2028-04-25 2028-05-29			
<b>CON2530 Installation and Test of Equipment</b> 2028-04-25 2028-05-29			
<b>S00 Aluminum Reduction Plant (Alumina Conveying System) Installation Package (f)</b> 2026-07-26 2029-08-13			
<b>CON2540 Installation Subcontractors Selection and Award</b> 2026-07-26 2026-10-24			
<b>CON2550 Advance Payment</b> 2026-10-24 2026-12-08			
<b>CON2560 Installation Subcontractor Mobilize on Site</b> 2026-12-08 2027-05-07			
<b>Mechanical and E&amp;I Installation</b> 2027-06-20 2029-08-13			
<b>E01 Raw Material Conveying system</b> 2028-05-25 2028-10-24			
<b>CON2570 Equipment Installation and Test</b> 2028-05-25* 2028-09-24			
<b>CON2580 No Load Test</b> 2028-09-25 2028-10-24			
<b>S03 Alumina Storage</b> 2028-02-09 2028-10-24			
<b>CON2590 Silo Erection</b> 2028-02-09 2028-07-24			
<b>CON2600 Installation and Test of Mechanical/Electrical Equipment and Instrumentation</b> 2028-06-25 2028-09-24			
<b>CON2610 No Load Test</b> 2028-09-25 2028-10-24			
<b>S0401 Alumina Conveying System and Daly Silo</b> 2027-07-30 2028-10-14			
<b>Steel Silo Erection</b> 2027-07-30 2028-02-20			
<b>CON2620 Daly Silo 1-1</b> 2027-07-30 2027-10-09			
<b>CON2630 Daly Silo 1-2</b> 2027-11-16 2028-01-14			
<b>CON2640 Daly Silo 1-3</b> 2027-12-21 2028-02-20			
<b>Installation and Test of Mechanical/Electrical Equipment and Instrumentation System</b> 2028-06-04 2028-08-13			
<b>CON2650 chute and Equipment 1-1</b> 2028-06-25 2028-07-24			
<b>CON2660 chute and Equipment 1-2</b> 2028-07-15 2028-08-13			
<b>CON2670 chute and Equipment 1-3</b> 2028-06-04 2028-07-19			
<b>No Load Test</b> 2028-08-25 2028-10-14			
<b>CON2680 No Load Test</b> 2028-08-25 2028-10-14			
<b>S0402 Alumina Conveying System and Daly Silo</b> 2028-04-04 2029-08-13			
<b>Steel Silo Erection</b> 2028-04-04 2029-01-29			
<b>1230 Daly Silo 2-1</b> 2028-04-04 2028-06-03			
<b>1231 Daly Silo 2-2</b> 2028-05-25 2028-08-18			
<b>1232 Daly Silo 2-3</b> 2028-11-30 2029-01-29			
<b>Installation and Test of Mechanical/Electrical Equipment and Instrumentation System</b> 2028-05-25 2029-06-13			
<b>1234 Chute and Equipment to Alumina Silo</b> 2028-05-25 2028-08-24			
<b>1235 chute and Equipment 2-1</b> 2028-07-05 2028-08-03			
<b>1236 chute and Equipment 2-2</b> 2028-09-30 2028-10-30			
<b>1237 chute and Equipment 2-3</b> 2029-04-14 2029-06-13			
<b>No Load Test</b> 2029-06-14 2029-08-13			
<b>1238 No Load Test</b> 2029-06-14 2029-08-13			
<b>S0601 Super Dense Phase Conveying System (Reacted silo installation)</b> 2027-06-20 2028-01-25			
<b>Installation</b> 2027-06-20 2028-01-25			
<b>Reacted Alumina Silo</b> 2027-06-20 2028-01-25			
<b>CON2690 Reacted Alumina Silo 1-1</b> 2027-06-20 2027-08-18			
<b>CON2700 Reacted Alumina Silo 1-2</b> 2027-10-06 2027-12-05			
<b>CON2710 Reacted Alumina Silo 1-3</b> 2027-11-26 2028-01-25			
<b>S0602 Super Dense Phase Conveying System (Reacted silo installation)</b> 2028-05-10 2028-11-29			
<b>Installation</b> 2028-05-10 2028-11-29			
<b>Reacted Alumina Silo</b> 2028-05-10 2028-11-29			
<b>CON2720 Reacted Alumina Silo 2-1</b> 2028-05-10 2028-07-19			
<b>CON2730 Reacted Alumina Silo 2-2</b> 2028-07-20 2028-09-29			
<b>CON2740 Reacted Alumina Silo 2-3</b> 2028-09-25 2028-11-29			
<b>GTC, FTC, and CTC Installation Package (g)</b> 2026-11-21 2029-07-19			
<b>CON2750 Mechanical Subcontractor Mobilize on Site</b> 2026-11-21 2027-04-20			

Remaining Level of Effort

Actual Work

Critical Remaining Work

summary


Actual Level of Effort

Remaining Work

Milestone


Page 17 of 28

Project Schedule(Level 3)

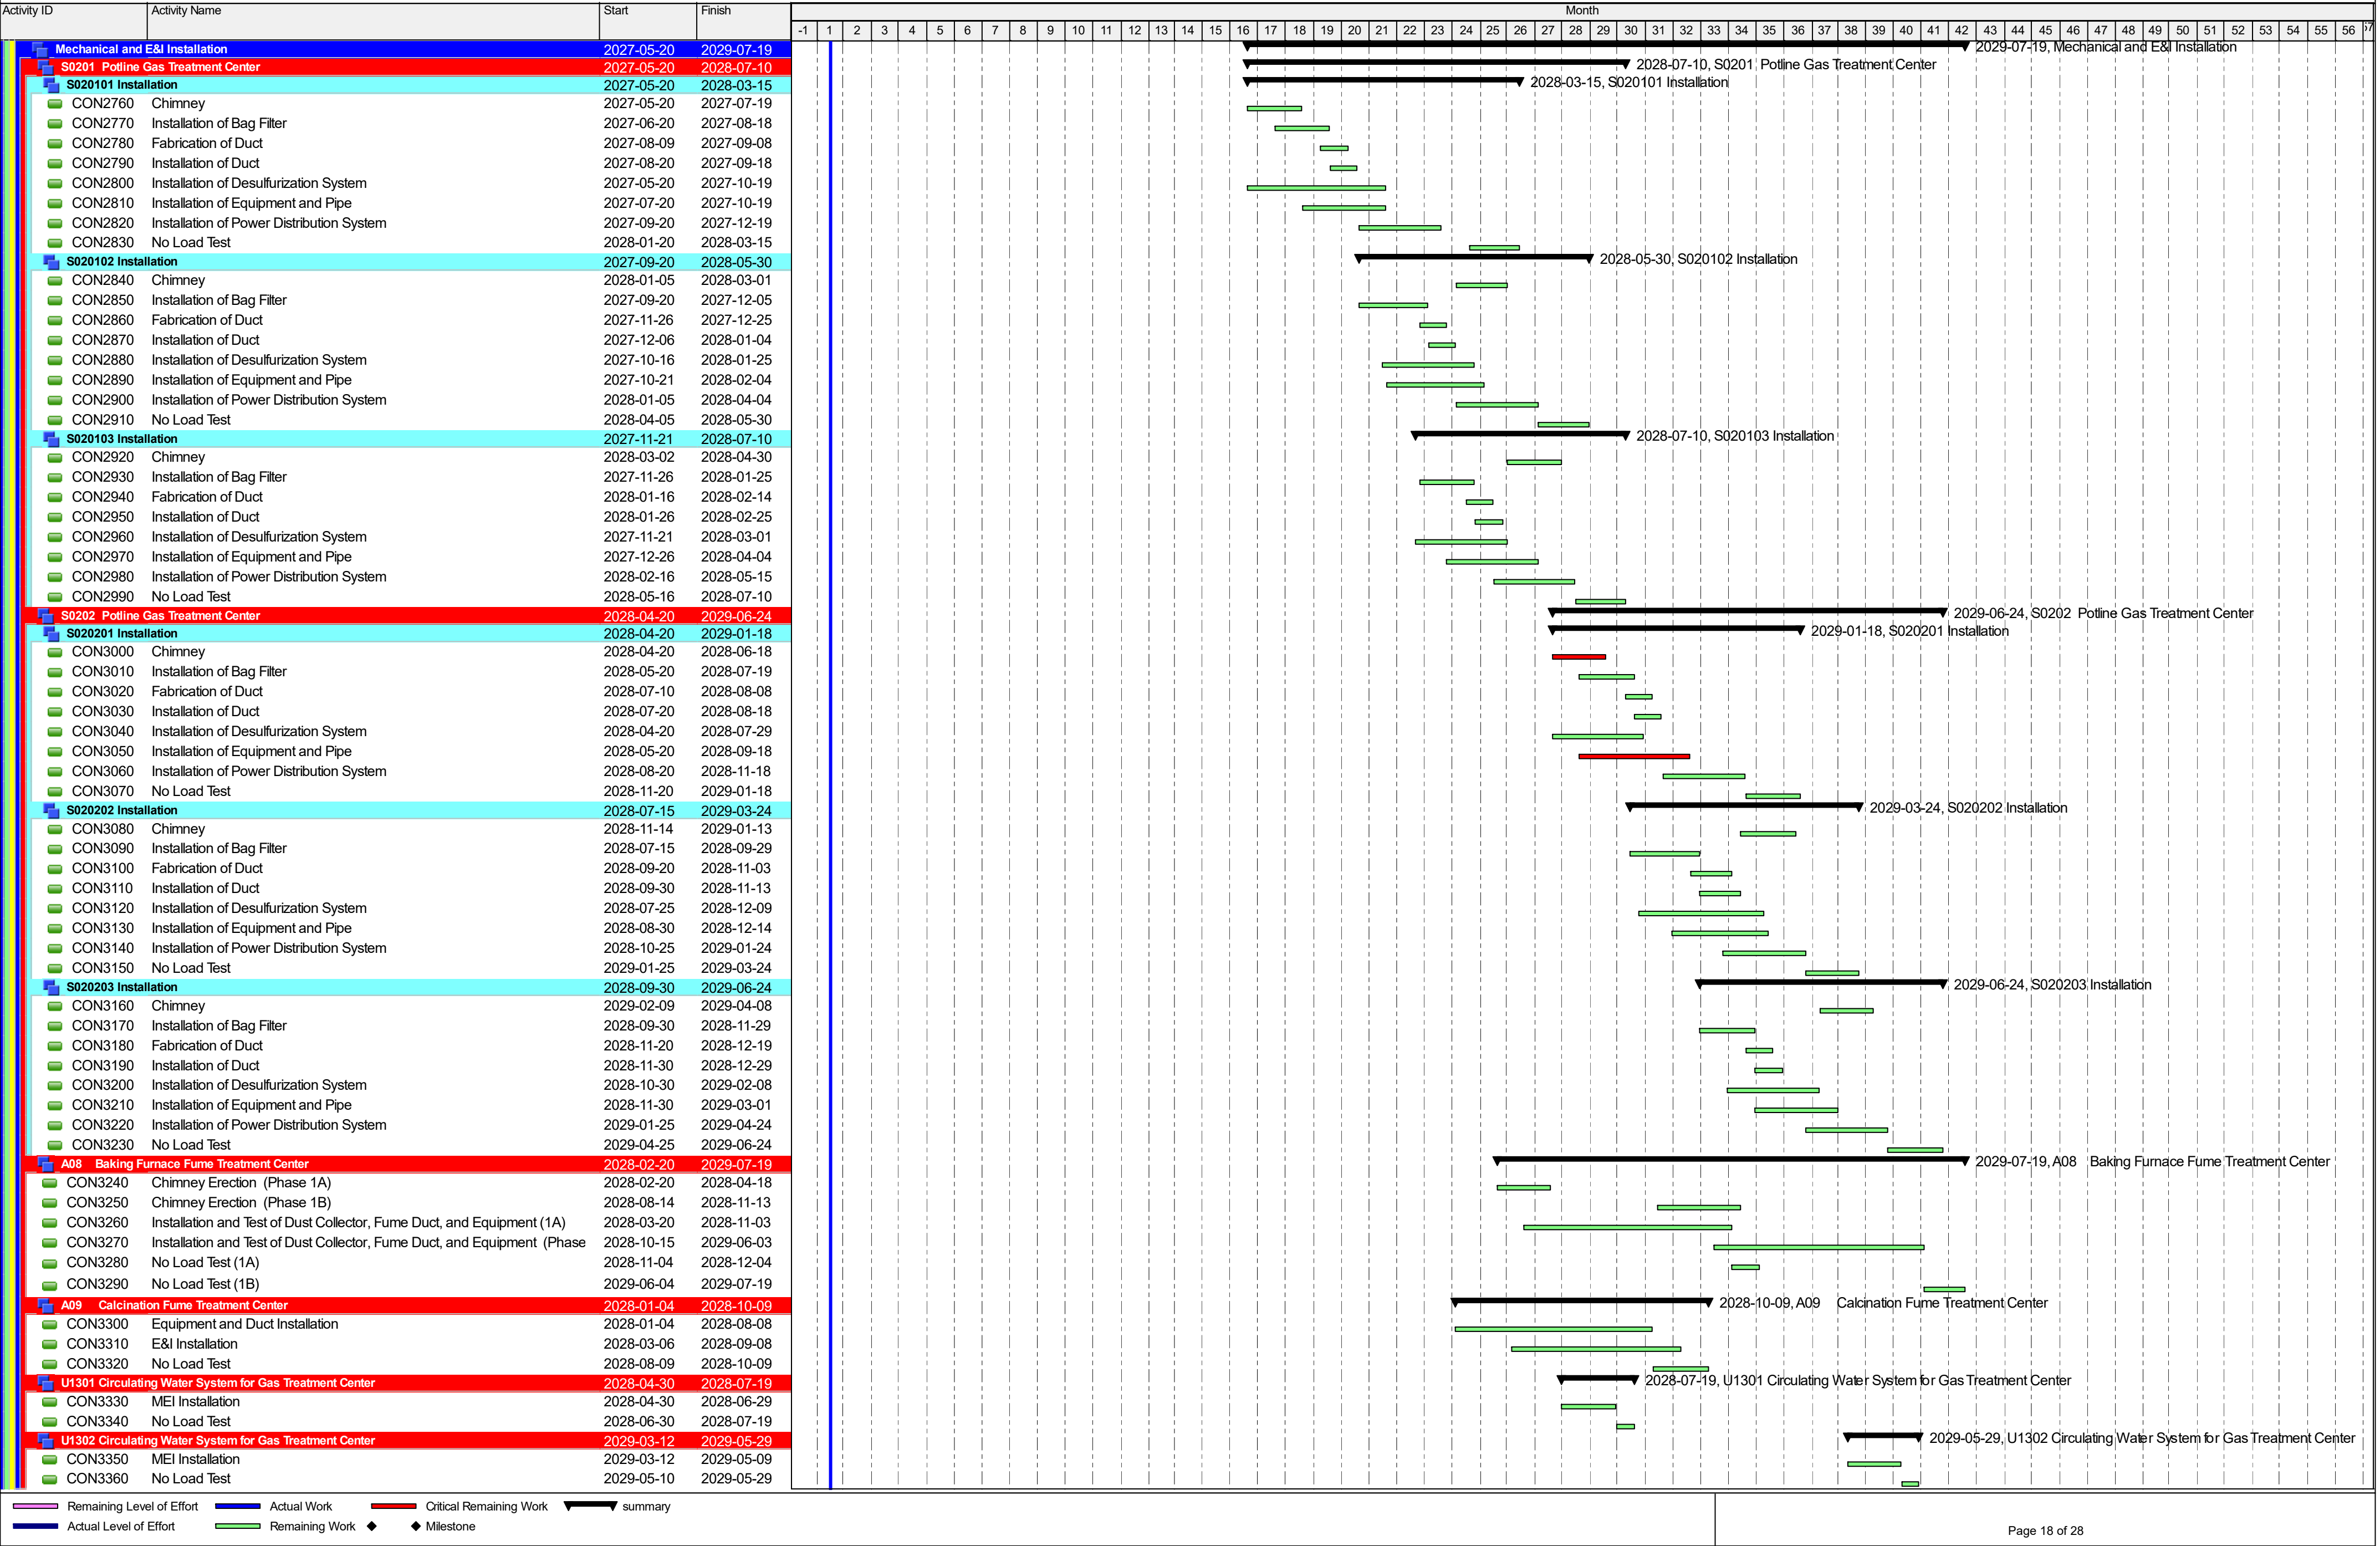



Project Schedule(Level 3)

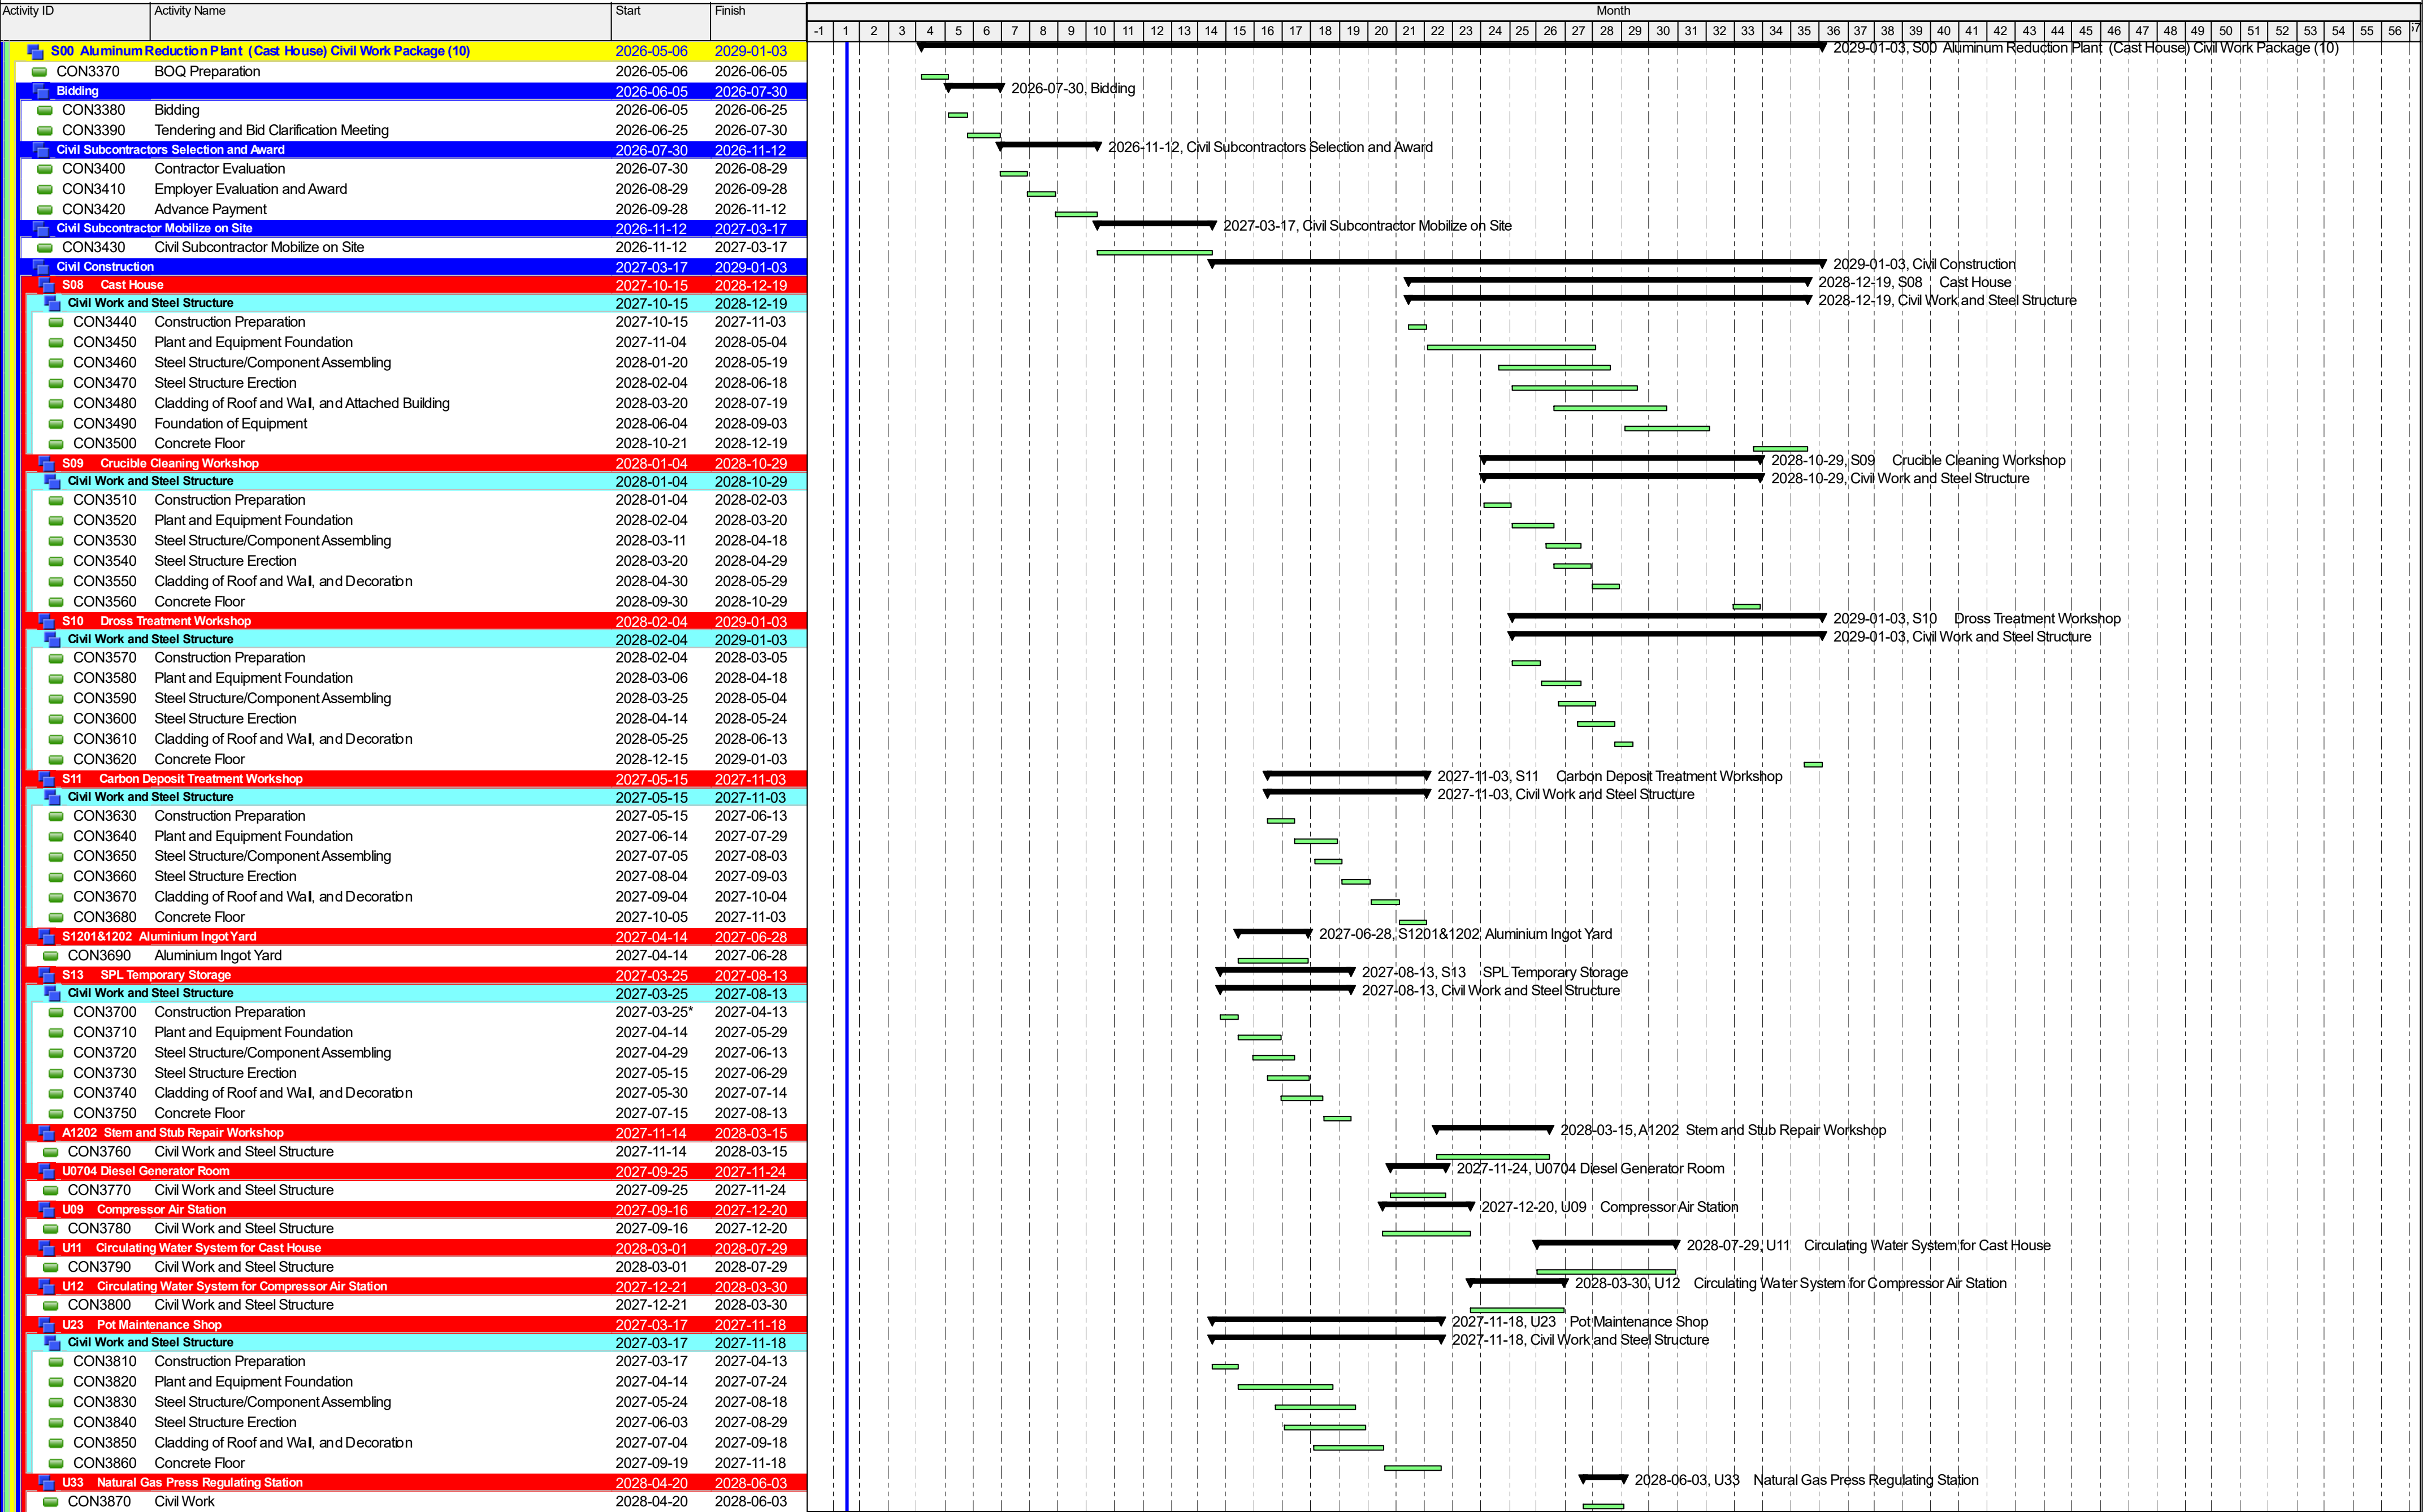

Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
M01 Comprehensive Office Building	Civil Work and Steel Structure	2027-12-05	2028-04-29
M02 Reduction Area Comprehensive Building	Civil Work and Steel Structure	2027-11-04	2028-03-29
M03 Dining Hall	Civil Work and Steel Structure	2028-02-14	2028-05-14
M04 Shower Room	Civil Work and Steel Structure	2028-03-16	2028-05-14
S00 Aluminum Reduction Plant (Cast House) Installation Package (h)	Installation Subcontractors Selection and Award Advance Payment Installation Subcontractor Mobilize on Site	2027-01-25	2029-01-18
Mechanical and E&I Installation	Installation Subcontractors Selection and Award Advance Payment Installation Subcontractor Mobilize on Site	2027-11-25	2029-01-18
S08 Cast House	Installation Overhead Crane MEI Installation and Cabling No Load Interlocking Test	2028-05-20	2029-01-18
S09 Crucible Cleaning Workshop	Equipment, Dust Collector System, and Electrical System No Load Test	2028-05-30	2028-10-29
S10 Dross Treatment Workshop	Equipment, Dust Collector System, and Electrical System No Load Test	2028-09-30	2029-01-13
S11 Carbon Deposit Treatment Workshop	Equipment, Dust Collector System, and Electrical System No Load Test	2028-09-09	2028-12-09
A1202 Stem and Stub Repair Workshop	Installation and Test	2028-10-30	2028-12-14
S13 SPL Temporary Storage	Equipment and Electrical System	2028-11-09	2028-11-29
U0704 Diesel Generator Room	Installation of Equipment	2027-11-25	2027-12-04
U09 Compressor Air Station	Installation of Equipment No Load Test	2027-12-21	2028-06-04
U11 Circulating Water System for Cast House	Installation of Equipment No Load Test	2028-07-30	2028-11-18
U12 Circulating Water System for Compressor Station	Installation of Equipment No Load Test	2028-03-31	2028-07-30
U33 Natural Gas Press Regulating Station	MEI Installation No Load Test	2028-06-04	2028-09-24
M01 Comprehensive Office Building	Installation of Air Conditioning and Ventilation Equipment	2028-04-30	2028-06-13
M02 Reduction Area Comprehensive Building	Installation of Air Conditioning & Ventilation and Lab Equipment	2028-03-30	2028-06-13
M03 Dining Hall	Installation of Air Conditioning and Ventilation Equipment	2028-05-15	2028-06-13
M04 Shower Room	Installation of Air Conditioning and Ventilation Equipment	2028-05-15	2028-06-29
S00 Aluminum Reduction Plant (Cathode Assembling) Installation Package (l)	Installation Subcontractors Selection and Award Advance Payment Installation Subcontractor Mobilize on Site Cathode Assembling	2027-02-23	2029-10-05
A00 Anode Plant (Anode Rodding Shop) Civil Work Package (11)	BOQ Preparation	2026-06-24	2028-12-14
Bidding	Bidding Tendering and Bid Clarification Meeting	2026-07-19	2026-09-06
Civil Subcontractors Selection and Award	Contractor Evaluation Employer Evaluation and Award Advance Payment	2026-09-06	2026-12-15
Civil Subcontractor Mobilize on Site	Civil Subcontractor Mobilize on Site	2026-12-15	2027-05-14
Civil Construction		2027-04-14	2028-12-14
S05 Fluoride Storage		2027-04-14	2027-08-03

Month

-1 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40 41 42 43 44 45 46 47 48 49 50 51 52 53 54 55 56 57

Remaining Level of Effort

Actual Work

Critical Remaining Work

summary

Actual Level of Effort

Remaining Work

Milestone

Page 20 of 28



Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish
CON4300	Construction Preparation	2027-04-14	2027-05-04
CON4310	Civil Work and Steel Structure	2027-05-05	2027-08-03
A0501	Butts Treatment Shop	2027-09-20	2028-03-19
Civil Work and Steel Structure		2027-09-20	2028-03-19
CON4320	Construction Preparation	2027-09-20	2027-10-19
CON4330	Plant and Equipment Foundation	2027-10-20	2028-01-18
CON4340	Silo Foundation	2027-10-20	2028-01-18
CON4350	Steel Structure/Component Assembling	2027-12-20	2028-02-03
CON4360	Steel Structure Erection	2027-12-25	2028-02-08
CON4370	Cladding of Roof and Wall, and Decoration	2028-01-24	2028-02-18
CON4380	Concrete Floor	2028-02-20	2028-03-19
A0502	Butts Treatment Shop	2028-03-16	2028-09-13
Civil Work and Steel Structure		2028-03-16	2028-09-13
CON4390	Construction Preparation	2028-03-16	2028-04-13
CON4400	Plant and Equipment Foundation	2028-04-14	2028-06-13
CON4410	Steel Structure/Component Assembling	2028-04-30	2028-06-13
CON4420	Steel Structure Erection	2028-06-14	2028-07-14
CON4430	Cladding of Roof and Wall, and Decoration	2028-07-15	2028-08-13
CON4440	Concrete Floor	2028-08-14	2028-09-13
A1001	Anode Rodding Shop	2027-05-14	2028-05-14
Civil Work and Steel Structure		2027-05-14	2028-05-14
CON4450	Construction Preparation	2027-05-14	2027-06-13
CON4460	Plant Foundation	2027-06-14	2027-10-13
CON4470	Steel Structure/Component Assembling	2027-06-29	2027-10-29
CON4480	Steel Structure, Roofing, and Cladding	2027-07-14	2027-11-13
CON4490	Indoor Pit and Equipment Foundation	2027-10-15	2028-02-13
CON4500	Flooring and Decoration	2028-02-14	2028-04-13
CON4510	Attached Building	2027-08-14	2027-10-19
CON4520	Completion of Civil Work	2028-04-14	2028-05-14
A1002	Anode Rodding Shop	2027-11-14	2028-12-14
Civil Work and Steel Structure		2027-11-14	2028-12-14
CON4530	Construction Preparation	2027-11-14	2027-12-14
CON4540	Plant Foundation	2027-12-15	2028-04-13
CON4550	Steel Structure/Component Assembling	2027-12-30	2028-04-25
CON4560	Steel Structure, Roofing, and Cladding	2028-01-14	2028-05-14
CON4570	Indoor Pit and Equipment Foundation	2028-05-15	2028-09-13
CON4580	Flooring and Decoration	2028-09-14	2028-11-13
CON4590	Attached Building	2028-03-16	2028-05-14
CON4600	Completion of Civil Work	2028-11-14	2028-12-14
A1101	Bath Treatment System	2028-02-13	2028-05-14
CON4610	Civil Work and Steel Structure	2028-02-13	2028-05-14
A1102	Bath Treatment System	2028-05-15	2028-08-13
CON4620	Civil Work and Steel Structure	2028-05-15	2028-08-13
U06	10kV Power Distribution Room in Anode Area	2027-11-04	2028-01-03
CON4630	Civil Work and Steel Structure	2027-11-04	2028-01-03
U0703	Diesel Generator Room	2028-02-03	2028-04-03
CON4640	Civil Work and Steel Structure	2028-02-03	2028-04-03
U15	Circulating Water System for Green Anode Shop	2028-03-20	2028-06-18
CON4650	Civil Work and Steel Structure	2028-03-20	2028-06-18
U16	Circulating Water System for Anode Rodding Shop	2028-03-16	2028-06-13
CON4660	Civil Work and Steel Structure	2028-03-16	2028-06-13
A00	Anode Plant (Anode Rodding Shop) Installation Package (I)	2026-10-15	2029-07-24
CON4670	Installation Subcontractors Selection and Award	2026-10-15	2027-01-22
CON4680	Advance Payment	2027-01-22	2027-03-08
CON4690	Installation Subcontractor Mobilize on Site	2027-03-08	2027-08-05
Mechanical and E&I Installation		2027-09-04	2029-07-24
S05	Fluoride Storage	2028-10-04	2028-12-04
CON4700	Installation	2028-10-04	2028-11-03
CON4710	No Load Test	2028-11-04	2028-12-04
A0501	Butts Treatment	2028-01-20	2028-08-03
Installation		2028-01-20	2028-08-03
CON4720	Silo Erection	2028-01-20	2028-05-19
CON4730	Equipment and Electrical System	2028-03-20	2028-06-13
CON4740	No Load Test	2028-06-14	2028-08-03
A0502	Butts Treatment	2028-09-14	2028-12-04
Installation		2028-09-14	2028-12-04
CON4750	Equipment and Electrical System	2028-09-14	2028-11-13
CON4760	Test	2028-11-14	2028-12-04
A1001	Anode Rodding Shop	2027-10-15	2028-10-14
Installation		2027-10-15	2028-10-14
CON4770	Steel Structure/Component of Suspension Chain Conveyor Assembling	2027-10-15	2027-12-14
CON4780	Frequency Induction Furnace, etc.	2028-01-14	2028-04-13
CON4790	Test	2028-04-14	2028-06-13
CON4800	Installation of Suspension Chain and Conveyor Equipment	2027-12-15	2028-03-15
CON4810	Installation of Working Stations, Electrical Equipment, and Instrumentation	2028-02-14	2028-07-14

Remaining Level of Effort

Actual Work

Critical Remaining Work

summary


Actual Level of Effort

Remaining Work

Milestone

Page 21 of

## Project Schedule(Level 3)

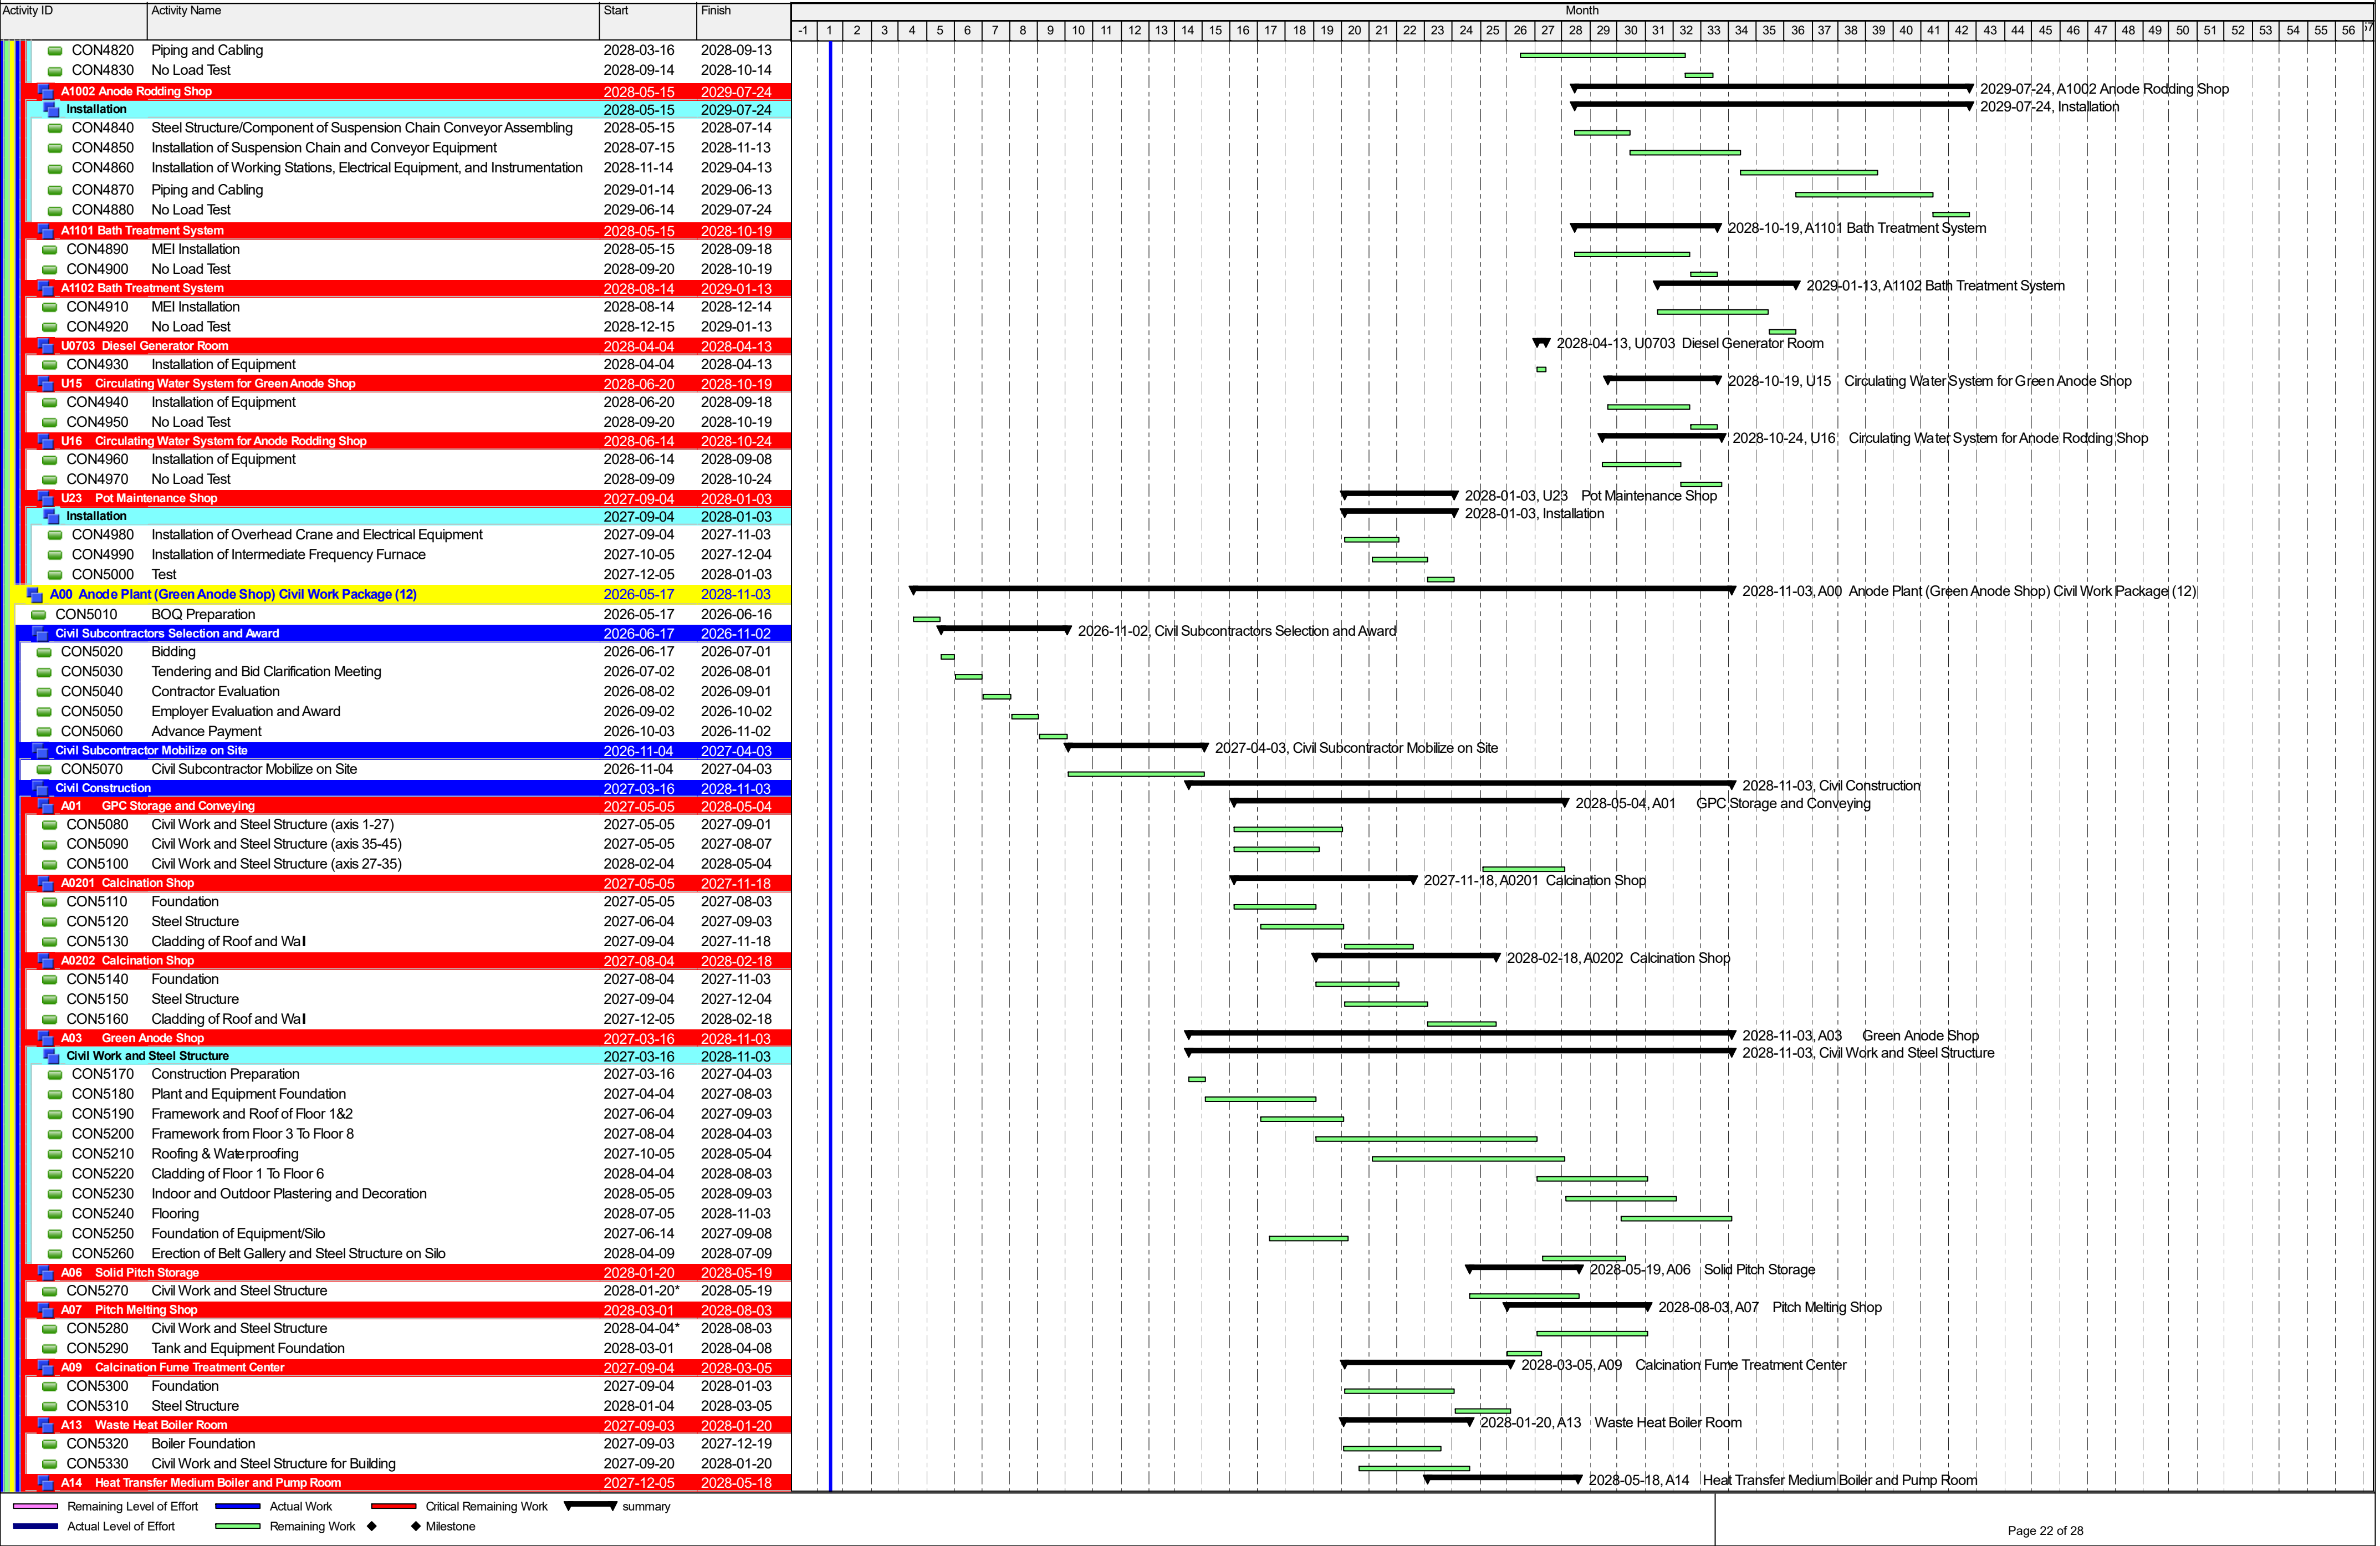



[illegible]

### Project Schedule(Level 3)


Activity ID	Activity Name	Start	Finish
CON5870	Transfer Station Equipment Foundation	2028-06-04	2028-08-03
CON5880	Baking Shop Foundation	2027-05-05	2027-09-03
CON5890	Steel Structure/Component Assembling	2027-05-20	2027-09-18
CON5900	Baking Shop Steel Structure Erection and Roofing 1-1	2027-06-04	2027-08-03
CON5910	Baking Shop Steel Structure Erection and Roofing 1-2	2027-08-04	2027-10-04
CON5920	Cladding and Decoration	2027-08-04	2028-01-03
CON5930	Furnace Foundation 1-1	2027-08-04	2027-11-03
CON5940	Furnace Foundation 1-2	2027-11-04	2028-02-03
CON5950	Grouping and Cleaning Machine Foundation 1-1	2028-04-04	2028-06-03
CON5960	Grouping and Cleaning Machine Foundation 1-2	2028-08-04	2028-10-04
A0402	Baking Furnace & Anode Transfer Station	2027-10-15	2029-04-13
Civil Work and Steel Structure		2027-10-15	2029-04-13
CON5970	Construction Preparation	2027-10-15	2027-11-13
CON5980	Transfer Station Foundation	2027-11-14	2028-02-13
CON5990	Transfer Station Steel Structure, Roof and Cladding	2027-12-15	2028-04-13
CON6000	Transfer Station Equipment Foundation	2028-12-15	2029-02-13
CON6010	Baking Shop Foundation 2-1	2027-11-14	2028-01-13
CON6020	Baking Shop Foundation 2-2	2028-01-14	2028-03-15
CON6030	Steel Structure/Component Assembling	2027-11-30	2028-03-29
CON6040	Baking Steel Structure Erection and Roofing 2-1	2027-12-15	2028-02-13
CON6050	Baking Steel Structure Erection and Roofing 2-2	2028-02-14	2028-04-13
CON6060	Cladding and Decoration	2028-02-14	2028-07-14
CON6070	Furnace Foundation 2-1	2028-02-14	2028-05-14
CON6080	Furnace Foundation 2-2	2028-05-15	2028-08-13
CON6090	Grouping and Cleaning Machine Foundation 2-1	2028-10-15	2028-12-14
CON6100	Grouping and Cleaning Machine Foundation 2-2	2029-02-14	2029-04-13
A08	Baking Furnace Fume Treatment Center	2028-01-04	2028-11-13
CON6110	Chimney Foundation (Phase 1A)	2028-01-04	2028-02-18
CON6120	Chimney Foundation (Phase 1B)	2028-05-15	2028-08-13
CON6130	Foundation of Dust Collector and Equipment (Phase 1A)	2028-02-20	2028-04-18
CON6140	Foundation of Dust Collector and Equipment (Phase 1B)	2028-08-14	2028-11-13
A00	Anode Plant (Baking Furnace) Installation Package (I)	2026-10-24	2029-08-13
CON6150	Installation Subcontractors Selection and Award	2026-10-24	2027-01-22
CON6160	Advance Payment	2027-01-22	2027-03-08
CON6170	Mechanical Subcontractor Mobilize on Site	2027-03-08	2027-08-05
Mechanical and E&I Installation		2027-11-04	2029-08-13
A0401	Baking Furnace & Anode Transfer Station	2027-11-04	2029-02-03
Installation		2027-11-04	2029-02-03
CON6180	Furnace Lining and Duct & Steel Structure Installation 1-1	2027-11-04	2028-04-03
CON6190	Furnace Lining and Duct & Steel Structure Installation 1-2	2028-03-06	2028-08-03
CON6200	Duct and Equipment Installation	2028-08-04	2028-10-02
CON6210	Grouping and Cleaning Machine Installation	2028-05-05	2028-11-03
CON6220	Stacking Crane Installation	2028-01-04	2028-05-04
CON6230	FAT Installation	2028-05-05	2028-11-27
CON6240	Installation of Electrical Equipment, Instrumentation and Piping	2028-06-04	2028-12-04
CON6250	Transfer Station Equipment Installation and Piping	2028-08-04	2029-01-03
CON6260	No Load Test	2029-01-04	2029-02-03
A0402	Baking Furnace & Anode Transfer Station	2028-05-15	2029-08-13
Installation		2028-05-15	2029-08-13
CON6270	Furnace Lining and Duct & Steel Structure Installation 2-1	2028-05-15	2028-10-14
CON6280	Furnace Lining and Duct & Steel Structure Installation 2-2	2028-09-14	2029-02-13
CON6290	Duct and Equipment Installation	2029-02-14	2029-04-13
CON6300	Grouping and Cleaning Machine Installation	2028-11-14	2029-05-14
CON6310	Stacking Crane Installation	2028-07-15	2028-11-13
CON6320	FAT Installation	2028-11-14	2029-06-08
CON6330	Installation of Electrical Equipment, Instrumentation and Piping	2028-12-15	2029-06-13
CON6340	Transfer Station Equipment Installation and Piping	2029-02-14	2029-07-14
CON6350	No Load Test	2029-07-15	2029-08-13
U00	Utilities (Rectifier Station) Civil Work Package (14)	2026-05-06	2029-01-03
CON6360	BOQ Preparation	2026-05-06	2026-06-05
Civil Subcontractors Selection and Award		2026-06-05	2027-03-17
CON6370	Bidding	2026-06-05	2026-07-20
CON6380	Contractor Evaluation	2026-07-20	2026-08-19
CON6390	Employer Evaluation and Award	2026-08-19	2026-09-18
CON6400	Advance Payment	2026-09-18	2026-11-02
CON6410	Civil Subcontractor Mobilize on Site	2026-11-02	2027-03-17
Civil Construction		2027-03-17	2029-01-03
E01	Raw Material Conveying system	2027-09-30	2028-07-09
CON6420	Civil Work and Steel Structure	2027-09-30*	2028-07-09
S03	Alumina Storage	2027-08-14	2028-03-10
CON6430	Construction Preparation	2027-08-14	2027-09-13
CON6440	Silo Foundation and Civil Work	2027-09-14	2028-03-10
A1201	Stem and Stub Repair Workshop	2027-06-04	202



Project Schedule(Level 3)

Activity ID	Activity Name	Start	Finish	Month																																																									
				-1	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57
U0101	330kV Power Distribution Device	2027-08-14	2028-05-04																																																										
	Civil Work and Steel Structure	2027-08-14	2028-05-04																																																										
	CON6460	2027-08-14	2027-09-13																																																										
	CON6470	2027-09-14	2028-04-03																																																										
	CON6480	2027-09-14	2028-05-04																																																										
U0102	330kV Power Distribution Device	2028-01-14	2028-10-14																																																										
	Civil Work and Steel Structure	2028-01-14	2028-10-14																																																										
	CON6490	2028-01-14	2028-02-13																																																										
	CON6500	2028-02-14	2028-09-13																																																										
	CON6510	2028-02-14	2028-10-14																																																										
U0201	330/10.5kV Substation and Center Control Room of the Smelter	2027-05-05	2028-01-29																																																										
	Civil Work and Steel Structure	2027-05-05	2028-01-29																																																										
	CON6520	2027-05-05	2027-06-03																																																										
	CON6530	2027-06-04	2027-12-04																																																										
	CON6540	2027-06-04	2028-01-29																																																										
U0202	330/10.5kV Substation and Center Control Room of the Smelter	2028-02-14	2028-11-13																																																										
	Civil Work and Steel Structure	2028-02-14	2028-11-13																																																										
	CON6550	2028-02-14	2028-03-15																																																										
	CON6560	2028-03-16	2028-05-14																																																										
	CON6570	2028-03-16	2028-11-13																																																										
U0301	Rectifier Station	2027-03-17	2028-03-24																																																										
	Civil Work and Steel Structure	2027-03-17	2028-03-24																																																										
	CON6580	2027-03-17	2027-04-15																																																										
	CON6590	2027-04-16	2028-01-24																																																										
	CON6600	2027-11-25	2028-03-24																																																										
U0302	Rectifier Station	2028-01-14	2029-01-03																																																										
	Civil Work and Steel Structure	2028-01-14	2029-01-03																																																										
	CON6610	2028-01-14	2028-02-13																																																										
	CON6620	2028-02-14	2028-10-04																																																										
	CON6630	2028-08-04	2029-01-03																																																										
U05	Emergency Oil Pools and Oil Storage Facilities	2028-01-30	2028-03-15																																																										
	CON6640	2028-01-30	2028-03-15																																																										
U0701&02	Diesel Generator Room	2028-02-03	2028-04-03																																																										
	CON6650	2028-02-03	2028-04-03																																																										
U10	Water Supply Pressurized Pump House	2027-08-14	2028-02-13																																																										
	CON6660	2027-08-14	2028-02-13																																																										
U18	Production Waste Water Treatment Station	2027-11-14	2028-04-13																																																										
	CON6670	2027-11-14	2028-04-13																																																										
U19	Domestic Waste Water Treatment Station	2028-01-14	2028-04-13																																																										
	CON6680	2028-01-14	2028-04-13																																																										
U22	Comprehensive Maintenance Workshop	2027-05-15	2027-09-08																																																										
	CON6690	2027-05-15	2027-09-08																																																										
U25	General Warehouse	2027-03-17	2027-10-04																																																										
	Civil Work and Steel Structure	2027-03-17	2027-10-04																																																										
	CON6700	2027-03-17	2027-04-13																																																										
	CON6710	2027-04-14	2027-06-13																																																										
	CON6720	2027-04-30	2027-06-29																																																										
	CON6730	2027-05-20	2027-08-03																																																										
	CON6740	2027-06-20	2027-09-03																																																										
	CON6750	2027-09-04	2027-10-04																																																										
U26	Process Vehicle Garage and Repair Shop	2028-01-04	2028-04-03																																																										
	CON6760	2028-01-04	2028-04-03																																																										
U00	Utilities (Rectifier Station) Installation Package (m)	2027-01-14	2029-07-18																																																										
	CON6770	2027-01-14	2027-04-14																																																										
	CON6780	2027-04-14	2027-05-29																																																										
	CON6790	2027-05-29	2027-10-26																																																										
	Mechanical and E&I Installation	2027-11-25	2029-07-18																																																										
A1201	Stem and Stub Repair Workshop	2028-09-14	2028-10-29																																																										
	CON6800	2028-09-14	2028-10-29																																																										
U0101	330kV Power Distribution Device	2028-02-05	2028-08-04																																																										
	Installation	2028-02-05	2028-08-04																																																										
	CON6810	2028-02-05	2028-08-04																																																										

Project Schedule(Level 3)

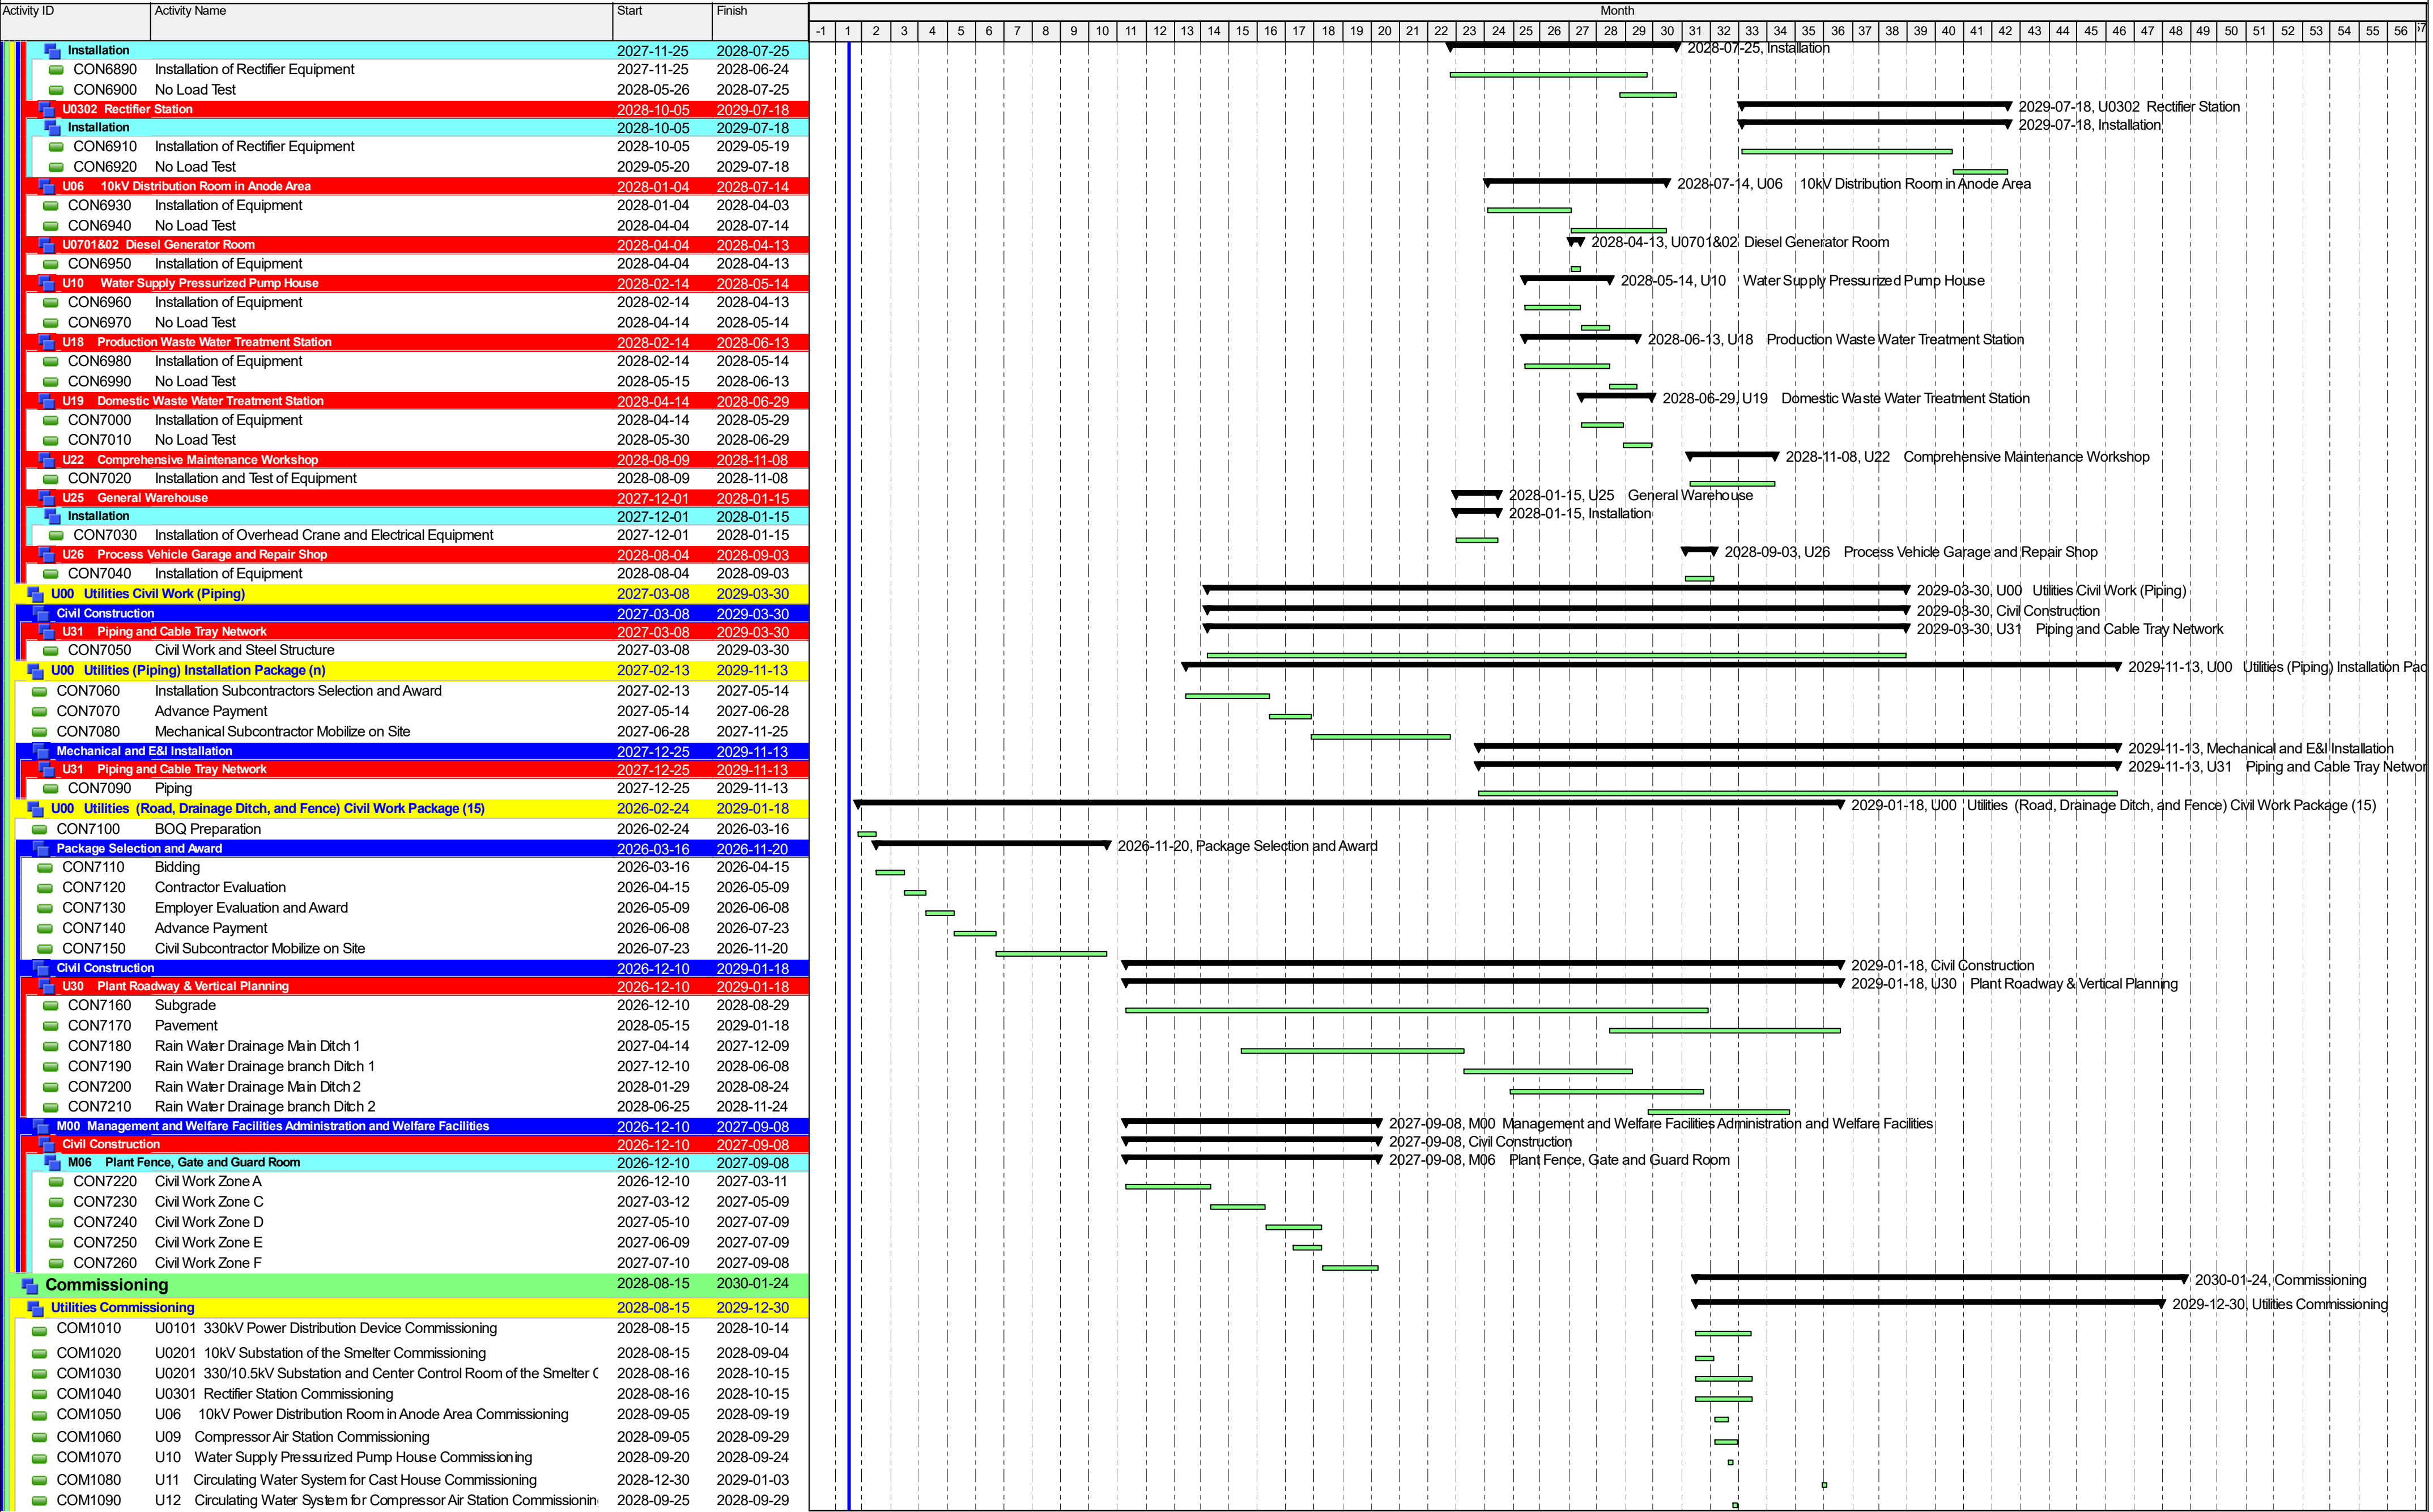



[illegible]

Project Schedule(Level 3)				
Activity ID	Activity Name	Start	Finish	Month
				-1 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40 41 42 43 44 45 46 47 48 49 50 51 52 53 54 55 56 57
TO1150	U0102 330kV Power Distribution Device Trial Operation	2029-09-15	2029-09-29	
TO1160	U0202 10kV Substation of the Smelter Trial Operation	2029-08-05	2029-08-24	
TO1170	U0202 330/10kV Substation and Center Control Room of the Smelter Tri	2029-09-15	2029-09-29	
TO1180	U0302 Rectifier Station Trial Operation	2029-09-18	2029-10-02	
TO1190	Other Utilities Trial Operation	2029-10-26	2029-12-15	
Phase 1A Anode System Trial Operation		2028-12-01	2029-05-30	
TO1200	A01 GPC Storage and Conveying Trial Operation	2028-12-01	2028-12-15	
TO1210	A0201 Calcination Shop Trial Operation	2028-12-11	2029-02-19	
TO1220	A03 Green Anode Shop Trial Operation	2029-02-21	2029-03-30	
TO1230	A0401 Baking Furnace & Anode Transfer Station Trial Operation	2029-03-31	2029-05-30	
TO1240	A0501 Butts Treatment Trial Operation	2029-01-04	2029-01-29	
TO1250	A06 Solid Pitch Storage Trial Operation	2029-01-05	2029-01-09	
TO1260	A07 Pitch Melting Shop Trial Operation	2029-01-05	2029-02-19	
TO1270	A08 Baking Furnace Fume Treatment Center (Phase 1A) Trial Operati	2029-03-31	2029-05-30	
TO1280	A09 Calcination Fume Treatment Center Trial Operation	2028-12-11	2029-02-08	
TO1290	A1001 Anode Rodding Shop Trial Operation	2029-01-04	2029-02-03	
TO1300	A13 Waste Heat Boiler Room Trial Operation	2028-12-11	2029-01-30	
TO1310	A14 Heat Transfer Medium Boiler and Pump Room Trial Operation	2028-12-11	2029-01-30	
Phase 1B Anode System Trial Operation		2029-06-04	2029-12-04	
TO1320	A0202 Calcination Shop Trial Operation	2029-06-04	2029-08-13	
TO1330	A0402 Baking Furnace & Anode Transfer Station Trial Operation	2029-10-05	2029-12-04	
TO1340	A08 Baking Furnace Fume Treatment Center (Phase 1B) Trial Operati	2029-10-05	2029-11-03	
TO1350	A1002 Anode Rodding Shop Trial Operation Trial Operation	2029-10-21	2029-11-09	
Phase 1A Reduction System Trial Operation		2028-12-05	2030-02-14	
TO1360	E01 & S05 Trial Operation	2028-12-05	2028-12-09	
TO1370	S03 Alumina Storage Trial Operation	2028-12-07	2028-12-11	
TO1380	S0201 Potline Gas Treatment Center & U13 Trial Operation	2028-12-21	2029-04-24	
TO1390	S0401 Alumina Conveying System and Daily Silo Trial Operation	2028-12-12	2028-12-20	
TO1400	S0601 Super Dense Phase Conveying System Trial Operation	2028-12-31	2029-02-24	
TO1410	S08 Cast House Trial Operation	2029-04-06	2029-04-10	
TO1420	Phase 1A Pots Baking and Start-up	2029-04-01	2029-11-14*	
TO1430	Fine Tune	2029-11-15	2030-02-14	
Phase 1B Reduction System Trial Operation		2029-10-25	2030-08-12	
TO1440	S0202 Potline Gas Treatment Center & U13 Trial Operation	2029-11-20	2030-03-24	
TO1450	S0402 Alumina Conveying System and Daily Silo Trial Operation	2029-10-25	2029-11-14	
TO1460	S0602 Super Dense Phase Conveying System Trial Operation	2029-11-30	2030-01-24	
TO1470	Phase 1B Pots Baking and Start-up	2030-02-11	2030-08-12*	
